



July 30, 2016

Director of the Division of Enforcement
Department for Environmental Protection
300 Fair Oaks Lane
Frankfort, KY 40601

Chief, Environmental Enforcement Section
Environmental and Natural Resources Division
U.S. Department of Justice
601 D street NW
Washington, DC 20005
DOJ Case No. 90-5-1-1-08591

Ms. Denisse Diaz, Chief
NPDES Permitting and Enforcement Branch
U.S. Environmental Protection Agency, Region 4
Atlanta Federal Center
61 Forsyth Street, S.W.
Atlanta, Georgia 30303

Re: Consent Decree Case No. 2:05-cv-00199-WOB

To Whom It May Concern:

Pursuant to the above-referenced Consent Decree, Sanitation District No. 1 (SD1) is required to submit quarterly reports that demonstrate SD1's compliance with the Consent Decree:

42. Quarterly Reports. The District shall submit to the Cabinet/EPA a quarterly report that describes the District's progress in complying with this Consent Decree for the previous quarter no later than thirty days after the end of each calendar quarter. The first such report shall be submitted to the Cabinet/EPA no later than thirty days after the second full quarter after entry of this Consent Decree.

Information contained within the enclosed Quarterly Report describes SD1's compliance with Consent Decree Case No. 2:05-cv-00199-WOB for the period of April 1, 2016 through June 30, 2016. The report also contains an outlook for the upcoming calendar quarter period of July 1, 2016 through September 30, 2016.

Page 2
July 30, 2016

A certification as required by the Consent Decree is also enclosed (Consent Decree paragraph 38).

To the best of my knowledge and belief, the enclosed report is true, accurate, and complete, and further demonstrates SD1's commitment to the mission of protecting and enhancing the water resources and quality of life in Northern Kentucky.

If you have any questions or concerns, do not hesitate to contact me at 859-578-6762 or by e-mail at mwurschmidt@sd1.org.

Best regards,



Mark W. Wurschmidt
Interim Executive Director

MWW/wck
Enclosures

Sanitation District No. 1
July 30, 2016

Consent Decree
Quarterly Report No. 35
(April 1, 2016 through July 30, 2016)



(This page intentionally left blank for double-sided printing.)

CERTIFICATION

Consent Decree Quarterly Report No. 35
Consent Decree Case No. 2:05-cv-00199-WOB

I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering such information, the information submitted is, to the best of my knowledge and belief, true, accurate and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

Mark W. Wurschmidt
Mark W. Wurschmidt
Interim Executive Director

7/28/16
Date

COMMONWEALTH OF KENTUCKY

)ss.

COUNTY OF Kenton

The foregoing instrument was acknowledged before me this 28 day of July, 20 16 by Mark W. Wurschmidt, Interim Executive Director of Sanitation District No. 1.

Angela M. Cook
NOTARY PUBLIC

Kenton County, Kentucky

My commission expires: 7-30-16



(This page intentionally left blank for double-sided printing.)

CONSENT DECREE QUARTERLY REPORT NO. 35

July 30, 2016



Sanitation District No. 1
1045 Eaton Drive
Ft. Wright, KY 41017

TABLE OF CONTENTS

SECTION 1. INTRODUCTION.....	1
1.1 Purpose	1
1.2 Report Period.....	1
1.3 Consent Decree Compliance Schedule	1
 SECTION 2. OVERFLOW DATA.....	 2
2.1 SSOs Due to Wet Weather Capacity Issues.....	6
2.2 SSOs Due to Operational Issues	9
2.3 Wet Weather CSOs	12
2.4 Dry Weather CSOs	12
2.5 Building Backups	12

APPENDICES

APPENDIX A: Consent Decree Compliance Schedule

APPENDIX B: Watershed Improvement Projects

APPENDIX C: Cumulative and Annual Overflow Data

APPENDIX D: Recurring Wet Weather SSOs

APPENDIX E: Wet Weather CSOs

FIGURES

Figure 2.1 SSO due to Vandalized Manhole

Figure 2.2 Occurrences of SSO due to Operational Issues per Cause (April 1, 2016 through June 30, 2016)

Figure 2.3 Gallons of SSO due to Operational Issues per Cause (April 1, 2016 through June 30, 2016)

Figure 2.4 Building Backups: Public System vs. Other Causes (April 1, 2016 through June 30, 2016)

Figure 2.5 Causes of Public System Related Building Backups (April 1, 2016 through June 30, 2016)

TABLES

Table 2.1 Summary of Storm Events (April 1, 2016 through June 30, 2016)

Table 2.2 Discharges from Consent Decree Pump Stations, due to Lack of Capacity during Wet Weather (April 1, 2016 through June 30, 2016)

LIST OF ACRONYMS AND ABBREVIATIONS

Cabinet	Kentucky Energy and Environment Cabinet
CSAP	Continuous Sewer Assessment Program
CSO	Combined Sewer Overflow
CVG	Cincinnati-Northern Kentucky International Airport
EPA	U.S. Environmental Protection Agency
KDOW	Kentucky Division of Water
SD1	Sanitation District No. 1
SORP	Sewer Overflow Response Plan
SSO	Sanitary Sewer Overflow

SECTION 1. INTRODUCTION

1.1 Purpose

This Quarterly Report is submitted to fulfill the requirements of Sanitation District No. 1's (SD1) Consent Decree, as entered on April 18, 2007. This Consent Decree is a legal agreement with the U.S. Environmental Protection Agency (EPA) and the Kentucky Energy and Environment Cabinet (Cabinet). The purpose of the Consent Decree is to address sanitary sewer overflows (SSOs) in SD1's sanitary sewer system and combined sewer overflows (CSOs) in the combined sewer system, in an effort to improve water quality throughout SD1's service area. Specifically, Section V Reporting Requirements, states that:

42. Quarterly Reports. The District shall submit to the Cabinet/EPA a quarterly report that describes the District's progress in complying with this Consent Decree for the previous quarter no later than thirty days after the end of each calendar quarter.

1.2 Report Period

Information contained within this report describes SD1's compliance with Consent Decree Case No. 2:05-cv-00199-WOB for the period of April 1, 2016 through June 30, 2016. This report also contains an outlook for the upcoming calendar quarter period of July 1, 2016 through September 30, 2016.

1.3 Consent Decree Compliance Schedule

A comprehensive compliance schedule for meeting the requirements of the Consent Decree can be found in Appendix A. A more detailed listing of the projects and activities conducted to comply with the requirements of the Consent Decree, including schedules, project updates for the current reporting period, and planned activity for the subsequent quarter, can be found in Appendix B.

Additionally, Appendix B provides a schedule of the projects proposed in the first five years of the Watershed Plans for Northern Kentucky, as well as status updates on CSO

and SSO reduction projects that have not been formally proposed. The Watershed Plans were submitted on March 31, 2011, approved by the Cabinet and EPA in a letter dated February 14, 2014, and resubmitted March 14, 2014 with agreed to revisions, as requested in the February 14, 2014 letter.

Initial Watershed Projects

As shown in Appendix B, SD1 has completed its Initial Watershed Projects. A request to remove a project (Western Regional – Richwood C-039-00) was included in the revised Watershed Plans, submitted on March 31, 2011. Approval of the request to remove the project was granted in a letter dated May 13, 2013 from the Cabinet and EPA. SD1 submitted its final Initial Watershed Projects Annual Report on June 7, 2013.

Pump Station Operation Plan for Backup Power

As shown in Appendix B, SD1 has completed the Pump Station Operation Plan for Backup Power, before of the Consent Decree deadline of December 31, 2015. SD1 submitted its Pump Station Operation Plan for Backup Power on December 14, 2007 and received regulatory approval on May 14, 2008. Of the 127 pump stations identified in the plan, 15 have been permanently eliminated, and 112 have fully implemented backup power solutions to mitigate overflows due to power failures during dry weather.

The schedule provided in Appendix B of this report only identifies 110 pump stations, because 17 of the 127 pump stations that required backup power were completed prior to the approval of the plan in 2007. The 17 projects that were identified as complete in Table 3.1 of the Pump Station Operation Plan for Backup Power, submitted on December 14, 2007, are not included in the final schedule provided in Appendix B of this report.

SECTION 2. OVERFLOW DATA

This section of the Quarterly Report presents SD1's estimates of overflow activity in the collection systems.

Overflow Categories

For reporting and system performance measurement purposes, SD1 has categorized sewer overflows throughout the service area into five distinct categories:

- *SSOs Due to Wet Weather Capacity Issues* – Recurring and inactive overflows from SD1’s sanitary sewer system due to a lack of capacity during wet weather. This category includes wet-weather discharges at pump stations that may or may not have a constructed bypass. Overflows are determined to be “recurring” if they have been observed to overflow twice in a running twelve month period. Overflows are determined to be “inactive” until they occur more than once in a running twelve month period. Inactive overflows are generally under investigation as suspected or predicted hydraulic model overflow points in the collection system.
- *SSOs Due to Operational Issues* – Overflows from SD1’s sanitary sewer system, including pump stations that are not a result of wet weather capacity issues. Many of these are one-time, dry-weather occurrences caused by temporary system issues that are investigated and corrected as soon as practicable.
- *Wet Weather CSOs* – Wet-weather discharges from the combined sewer system.
- *Dry Weather CSOs* – Dry-weather discharges from the combined sewer system.
- *Building Backups* – The release of raw sewage from a service lateral into a building in SD1’s service area. Building backups can be caused by several factors, such as constrained capacity during wet weather, or a blockage in the private service lateral or public main line. Building backups can be determined to be associated with the public sewer system or can be due to other causes beyond the control of SD1.

Quantitative Estimates

SD1 uses three general methods for developing quantitative overflow estimates:

- Field inspections shortly after wet-weather events to identify activations. This inspection program has been in place since 2005 and can be expanded, as warranted, for record keeping and sewer overflow response cleanup. SD1’s Collection Systems Department and Infrastructure Capital Planning Department continue to perform routine inspections after rain events at prioritized recurring, inactive, and suspected SSO locations to confirm overflow activity, and assess the

need for sewer overflow response cleanup. This is part of SD1's continuous effort to characterize and verify overflows throughout the collection systems, and to ensure that they are recorded accurately and cleaned up after rain events. Proper characterization of overflows ensures that the hydraulic models SD1 utilizes are maintained and improved upon, which helps identify the most appropriate and effective solutions for mitigation.

- Simple hydraulic estimating using Manning's Gravity Flow and Pipe Calculation to report overflows from pump stations with constructed bypasses, and industry standard volume estimations techniques and calculations are used for spills or for any witnessed overflow from a manhole. The only exceptions to this calculation methodology are at the Lakeview Pump Station and, as of January 2016, at the Highland Heights Pump Station. These two pump stations have flow meters in the bypass pipes that will be used as the primary sources of volumes estimates. If a flow meter malfunctions during an overflow, the Manning's Gravity Flow and Pipe Calculation will be used as the default method of volume estimation. These methods have been used historically for reporting purposes.
- SD1's hydraulic models are used for quarterly activation and volume estimations of wet-weather CSOs and SSOs. SD1 completed a year-long flow monitoring program in 2008, consisting of more than 245 flow meters and 45 rain gauges installed throughout the combined and separated systems, to update the calibration of SD1's system-wide hydraulic models. This calibration was undertaken to provide a model network that could confidently be used as an accurate tool in preparing SD1's Watershed Plans. Currently, SD1 maintains approximately 70 flow meters and 25 rain gauges throughout the year, which are used to continuously update and refine the models. Additionally, the models are being used to provide information about the current performance of SD1's system on a quarterly basis. With the historical and current flow monitoring and inspection data collected, SD1 maintains its highly calibrated network of hydraulic models to provide an accurate representation of the sewer systems. These modeling and monitoring tools confidently provide estimates of overflow activations and volumes from the sewer systems as a result of wet weather. The models are continuously revised to incorporate rehabilitation and maintenance activities, completed capital projects, private developments, data gathered from

GPS surveys, and mapping of discovered infrastructure. This process ensures that the models are kept up-to-date and accurately reflect the current state of the collection systems. This approach is consistent with SD1's commitment to provide the best available information on overflow activity.

For this submittal, SD1 has collected rainfall data from a series of 23 rain gauges located across the system, to simulate the wet weather that occurred between April 1, 2016 and June 30, 2016. The results of the model simulations have been summarized and included in this report as estimates of the frequency and total volume of the overflow locations within SD1's service area, for this period. For the modeled locations, these results are not a summary of observed or confirmed activations, but are a confident estimate of the overflow statistics based on the calibrated and verified models.

Precipitation Data

Rainfall statistics are an important component of overflow reporting, as rainfall conditions represent an uncontrolled variable impacting SD1's wet-weather CSO and SSO activity. Quarterly CSO and SSO activations and volumes change over time, due to natural variations in rainfall patterns and antecedent moisture conditions. Over time, SD1 expects system improvements to show a clear trend in reduced overflow activity. However, reviewing overflow reports for any individual quarter, relative to the previous quarter, also requires careful review of the rainfall associated with each period, in order to understand the impact of shifting rainfall patterns. For this reason, storm event summaries are included in all overflow reporting submittals. The data in Table 2.1 is from the Cincinnati-Northern Kentucky International Airport (CVG) rain gauge, maintained by the National Weather Service, in northeast Boone County.

Table 2.1 Summary of Storm Events
(April 1, 2016 through June 30, 2016)

Month	Approximate # of Storm Events ¹	Rainfall (in)
April	11	4.99
May	14	2.68
June	11	2.48
Total	36	10.15

¹ A storm event is defined as at least 0.01" of rain with a minimum inter-event time of 7 hours.

The second quarter is usually the wettest quarter of the year. However, the second quarter of 2016 was drier than the first quarter, which was abnormally wet. The historical average of cumulative rainfall depth, at CVG, for the second quarter, from 1951 through 2005, is approximately 12.1 inches. For further comparison, the cumulative rainfall depth in the second quarter of the typical year (1970) is approximately 14.8 inches. The National Weather Service's recorded cumulative rainfall depth for the second quarter of 2016, 10.15 inches, is approximately 16 percent less than the 50-year average and approximately 31 percent less than the typical year's second quarter. The drier conditions in May and June produced the second lowest cumulative rainfall for the second quarter, since SD1 entered the Consent Decree in 2007. These dry conditions have generally contributed to less wet-weather overflows than normally observed during the spring.

The remainder of this section reports overflows that occurred throughout SD1's service area during the period of April 1, 2016 through June 30, 2016. Annual comparisons and a cumulative accounting of SD1's overflows from January 2008 through the current reporting period can be found in Appendix C.

2.1 SSOs Due to Wet Weather Capacity Issues

As previously described, this category includes recurring and inactive overflows from SD1's sanitary sewer system, due to lack of capacity during wet weather. This includes wet-weather discharges at pump stations that may or may not have a constructed bypass. Sanitary Sewer Overflows are determined to be "Recurring" if evidence of overflow is found at least twice in a twelve month period. Sanitary Sewer Overflows are classified as "Inactive" until evidence of overflow is confirmed more than once in a twelve month period. An Inactive SSO is generally under investigation for at least two years as a suspected or predicted hydraulic model overflow point in the collection system, until it is confirmed as a Recurring SSO or is eliminated.

Recurring Wet Weather SSOs

Modeled activation and volume statistics of SD1's 108 recurring wet-weather SSOs for the current reporting period can be found in Appendix D. The Recurring SSO list is updated annually in the April Quarterly Report to reflect the latest information from ongoing system characterization, based upon field inspections, flow monitoring, and

hydraulic modeling. A detailed list of structure numbers and transaction descriptions for the revisions made to the current Recurring SSO list for 2016 can be found in Quarterly Report No. 34.

Recurring Wet Weather SSO Pump Stations Listed in the Consent Decree

Along with the 108 recurring wet-weather SSOs, there are also 14 pump stations identified in the Consent Decree that have historically experienced recurring wet-weather capacity issues. Table 2.2 lists each of the 14 pump stations identified in Exhibit E of the Consent Decree, and demonstrates their observed quarterly wet-weather SSO occurrences and estimated discharge volumes.

Lakeview Pump Station has a metered bypass to calculate overflow volumes. However, the flow meter at the Lakeview Pump Station had a damaged probe that prevented accurate velocity measurements. SD1 replaced the damaged probe in early June, and the flow meter is currently working properly. The Manning's Gravity Flow and Pipe Calculation was used to estimate the volume of the one overflow from the Lakeview Pump Station that occurred in April.

**Table 2.2 Discharges from Consent Decree Pump Stations,
due to Lack of Capacity during Wet Weather
(April 1, 2016 through June 30, 2016)**

Name of Pump Station	Number of Wet-Weather Related Discharge Occurrences	Total Estimated Volume (gallons)
Lakeview	1	177,600
Alex-Licking	0	0
Allen Fork	0	0
Crestview	0	0
Harrison Harbor	0	0
Highland Acres	0	0
Kentucky Aire	0	0
Riley Road	0	0
Ripple Creek	0	0
South Hampton	0	0
South Park	0	0
Sunset	0	0
Taylorport	0	0
Union	0	0
TOTAL	1	177,600

Gray denotes where remedial measures have been completed for Exhibit E pump stations.

Wet Weather Overflow Evidence Found Upstream of the Allen Fork Pump Station

Between April 26, 2016 and May 1, 2016, approximately 2.5 inches of steady rain produced a storm event with a 5-day duration and a 4-month return period, according to the *Rainfall Frequency Atlas of the Midwest* (Huff & Angel, 1992). In accordance with SD1's post-wet weather inspection and SORP procedures, the former Recurring SSO 2390002 associated with the Allen Fork Pump Station was inspected for overflow evidence. During the storm event, SD1 did not have visual confirmation or a telemetry report from the pump station to indicate that there was a wet-weather overflow at the upstream manhole 2390002. However, less than a pound of residual sewer debris was found around the manhole, during the post-wet weather inspection on May 5, 2016. The residual overflow evidence was immediately cleaned up, and an overflow record was created in SD1's asset management software.

SD1 removed Recurring SSO 2390002 from the Recurring Wet Weather SSO List and reclassified it as Eliminated in Quarterly Report No. 30, submitted on April 30, 2015. The elimination of the SSO was based on two full years of post-wet weather inspections resulting in no overflow evidence found more than once during a 12-month period, following the implementation of remedial measures. The elimination of the Recurring SSO was recorded ahead of the Consent Decree Exhibit E deadline of December 31, 2015 to implement remedial measures at the Allen Fork Pump Station. The new overflow evidence indicates that there may be emergent maintenance issues within the collection system or at the pump station (see further discussion in Section 2.2). SD1 is currently evaluating the collection system and pump station to determine why the overflow occurred, and if further remedial measures at the pump station are warranted. A wireless ultra-sonic level sensor has been installed in manhole 2390002 to remotely monitor the site, and to alarm SD1 staff in real time if another wet-weather overflow is imminent. The overflow status of the manhole will be reevaluated with the next annual revision of the Recurring Wet Weather SSO List, to be submitted in Quarterly Report No. 38, due on April 30, 2017.

Wet Weather SSO Pump Stations Not Listed in the Consent Decree

In addition to tracking the recurring wet-weather SSOs at the pump stations listed in the Consent Decree, SD1 continuously monitors all pump stations throughout the service area for recurring wet-weather capacity issues.

During the current reporting period, Highland Heights Pump Station is the only pump station not listed in the Consent Decree where SD1 observed wet-weather capacity issues. As of January 2016, the estimated overflow volumes provided at the Highland Heights Pump Station have been calculated by a flow meter in the bypass pipe. Highland Heights Pump Station discharged eight times in the second quarter of 2016, for a combined total of approximately 2,093,100 gallons.

Inactive Wet Weather SSOs

No inactive wet-weather SSOs were observed by SD1 in the current reporting period.

2.2 SSOs Due to Operational Issues

This category of overflows includes discharges from SD1's sanitary sewer collection system and pump stations that are not a result of wet-weather capacity issues. Many of these are one-time, dry-weather occurrences caused by temporary system issues that are investigated and corrected as soon as possible.

All SSOs documented in this section were immediately acted upon and corrected, in accordance with SD1's SORP procedures. Additionally, all observed overflow events are recorded in Lucity, and are periodically reviewed to identify if any trends or localized problem areas exist that warrant the need for a larger-scale inspection or rehabilitation project.

During the current reporting period, there were a total of 12 SSOs due to operational issues throughout SD1's service area, resulting in a total estimated overflow volume of 484,600 gallons.

Pump Station Overflows

On April 20, 2016, the Highland Heights Pump Station spilled approximately 1000 gallons of SSO into the Ohio River, due to rags and debris that clogged two of the three pumps. SD1 vactored out all of the debris from the wet well and cleaned the affected pumps.

On May 31, 2016, the Allen Fork Pump Station experienced a telemetry system failure that spilled approximately 26,000 gallons of SSO from manhole 2390002 into the Allen Fork Creek. Within one hour of the failure, SD1 identified a corroded relay from the high

level alarm in the wet well, which prevented the proper activation of the station's bubbler system and backup control mode. The relay was replaced and a signal was reestablished with the Dry Creek Wastewater Treatment Plant within two hours of the failure. The spilled solids visible along the creek were raked up and vactored out. SD1 is currently evaluating if the failure of the telemetry system also contributed to wet-weather overflow evidence described in Section 2.2, which was found on May 5, 2016. A wireless ultra-sonic level sensor has been installed in manhole 2390002 to provide real-time, redundant monitoring to the repaired telemetry system.

Collection System Overflows

On April 7, 2016, while performing routine system maintenance, SD1 discovered a vandalized manhole along a tributary of Dry Creek, in the City of Erlanger. The manhole had been filled to the top with rocks. SD1 estimates that the blockage caused 395,000 gallons of SSO to spill, making it the largest observed overflow from the collection system in the second quarter. SD1 broke the blockage by jetting the manhole. To completely clear the blockage from the pipe, an entry was made to remove all the rocks and debris by hand. After the flow was returned to the pipe, SD1 recovered the visible solids from the creek and performed restoration of the contaminated soils. To prevent future vandalism of the system in the vicinity of this SSO, SD1 installed bolted-down lids on three manholes. Figure 2.1 is a photograph of the vandalized manhole prior to mitigation.


Figure 2.1 SSO due to Vandalized Manhole



The sewers where blockages produced SSOs were put into the Continuous Sewer Assessment Program (CSAP) to be inspected and cleaned as determined by the CSAP logic, which also provides appropriate next actions to address the cause of the blockages with regular maintenance routines.


Figure 2.2 demonstrates the primary causes of the SSOs due to operational issues, in the second quarter of 2016.

Figure 2.2 Occurrences of SSO due to Operational Issues per Cause
(April 1, 2016 through June 30, 2016)

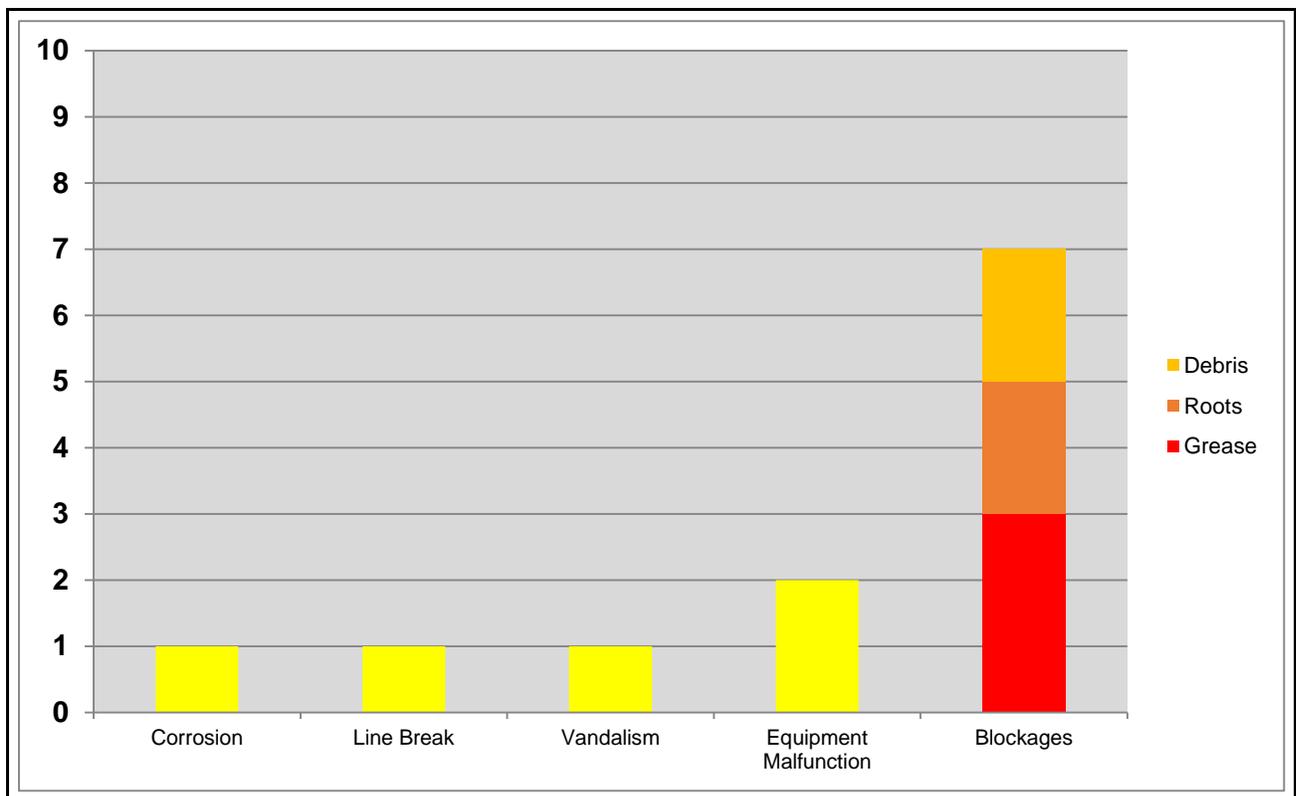

On the following page, Figure 2.3 demonstrates the corresponding estimated volumes of the SSOs due to operational issues, in the second quarter of 2016.

**Figure 2.3 Gallons of SSO due to Operational Issues per Cause
(April 1, 2016 through June 30, 2016)**

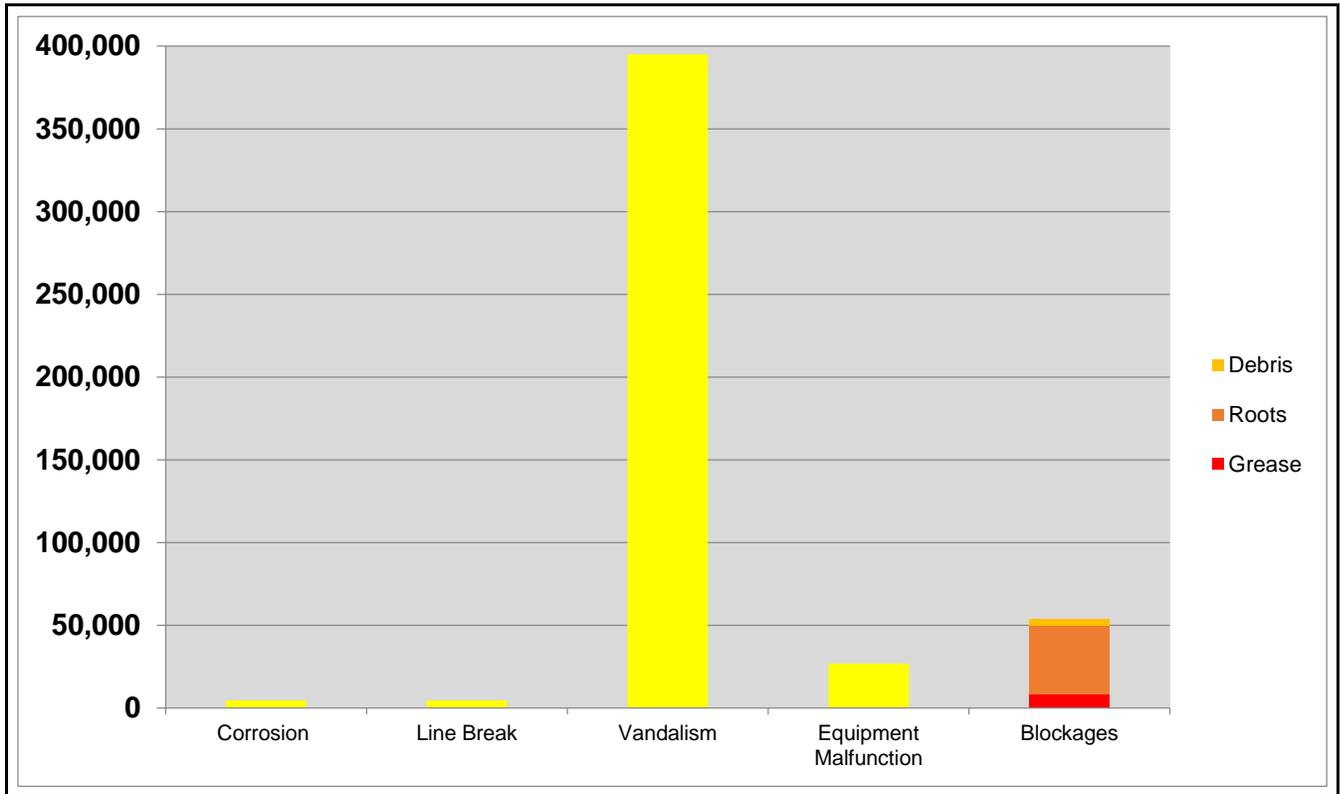

2.3 Wet Weather CSOs

Included in Appendix E are the modeled activation and volume statistics for SD1’s 95 CSOs in the second quarter of 2016.

2.4 Dry Weather CSOs


No dry-weather CSOs were detected by SD1 in the second quarter of 2016.

2.5 Building Backups

During the second quarter of 2016, there were approximately 109 building backups throughout SD1’s service area. Of these 109 backups, approximately 10 were determined to be related to the condition or operation of the public sewers and 99 were caused by other issues, as shown in Figure 2.4. The building backups that were not


related to the condition or operation of the public sewers were determined to be caused by blockages in private service laterals and internal plumbing.

Figure 2.4 Building Backups: Public System vs. Other Causes
(April 1, 2016 through June 30, 2016)

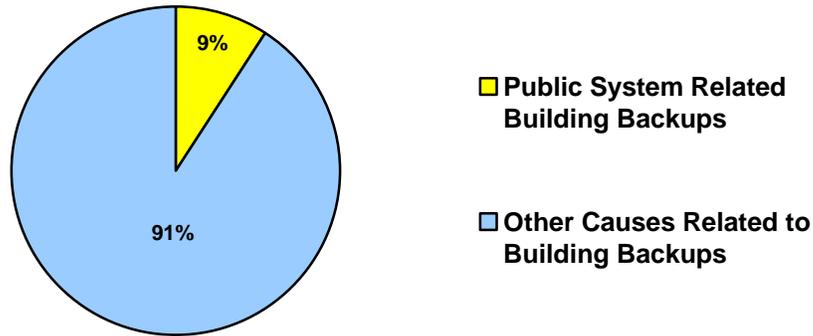

The causes of the 10 building backups determined to be related to the condition or operation of the public sewer lines are detailed in Figure 2.5.

Figure 2.5 Occurrences of Public System Related Building Backups per Cause
(April 1, 2016 through June 30, 2016)

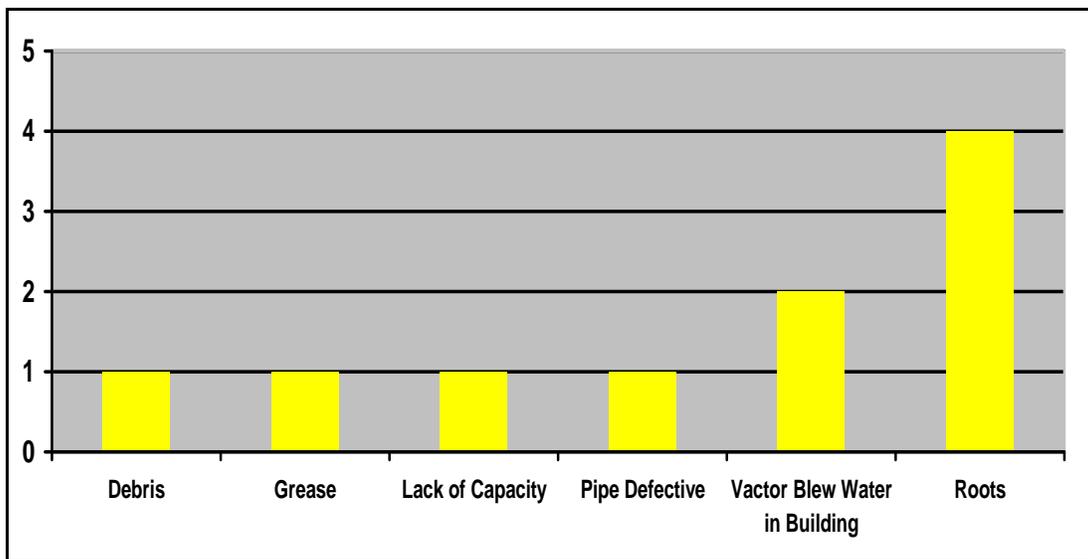

The sewers where blockages occurred were put into or updated in SD1’s CSAP, to be inspected and cleaned as determined by the program logic that provides appropriate next actions for maintenance issues.

All known building backups are recorded in Lucity and are periodically reviewed to identify if any trends or localized problem areas exist that warrant the need for a larger-scale inspection routine, rehabilitation, or repair project.

(This page intentionally left blank for double-sided printing.)

APPENDIX A:
Consent Decree Compliance Schedule

(This page intentionally left blank for double-sided printing.)

Consent Decree Compliance Schedule

CONSENT DECREE ACTIVITY		PERCENT COMPLETE	DUE DATE	DATE OF COMPLETION
ASSESSED STIPULATED PENALTY				
✓	\$14,000 for 9 DWOs occurring April 18, 2009 through June 30, 2010	100%	1/9/2011	12/21/2010
✓	\$22,000 for 11 DWOs occurring July 1, 2010 through June 30, 2014	100%	1/2/2015	12/8/2015
CIVIL PENALTY				
✓	Pay Civil Penalties to EPPC and US EPA	100%	06/18/07	06/18/07
CMOM PROGRAM REQUIREMENTS – 2007 through 2015				
✓	Submit CMOM Program Self-Assessment	100%	10/18/07	10/17/07
✓	Submit Grease Control Program	100%	10/18/07	09/17/07
✓	Submit Pump Station Backup Power Plan	100%	04/18/08	12/14/07
✓	Submit Sewer Overflow Response Plan (SORP)	100%	10/18/07	10/09/07
Submit CMOM Annual Report				
✓	CMOM Annual Report 1	100%	12/31/07	12/28/07
✓	CMOM Annual Report 2	100%	12/31/08	12/19/08
✓	CMOM Annual Report 3	100%	12/31/09	12/18/09
✓	CMOM Annual Report 4	100%	12/31/10	12/21/10
✓	CMOM Annual Report 5	100%	12/31/11	12/21/11
✓	CMOM Annual Report 6	100%	12/31/12	12/31/12
✓	CMOM Annual Report 7	100%	12/31/13	12/31/13
✓	CMOM Annual Report 8	100%	12/31/14	12/31/14
✓	CMOM Annual Report 9	100%	12/31/15	12/31/15
	CMOM Annual Report 10	0%	12/31/16	
Phased Grease Control Implementation				
✓	Phase 1 Tasks	100%	01/08/09	01/08/09
✓	Phase 2 Tasks	100%	01/08/10	01/08/10
✓	Phase 3 Tasks	100%	01/08/11	01/08/11
✓	Phase 4 Tasks / Full Implementation	100%	01/08/12	12/31/11
Complete Pump Station Backup Power Projects (110 Total)				
		100%	12/31/2015	10/30/15
Complete SORP Annual Review				
✓	SORP Annual Review 1	100%	05/14/09	07/10/09
✓	SORP Annual Review 2	100%	11/10/10	10/01/10
✓	SORP Annual Review 3	100%	11/10/11	11/10/11
✓	SORP Annual Review 4	100%	11/10/12	11/10/12
✓	SORP Annual Review 5	100%	11/10/13	11/08/13
✓	SORP Annual Review 6	100%	11/10/14	11/11/14
✓	SORP Annual Review 7	100%	11/10/15	11/10/15
	SORP Annual Review 8	0%	11/10/16	
INITIAL WATERSHED PROJECTS				
✓	Complete Initial Watershed Projects (51 Total)	100%	12/31/14	06/06/12
Submit Initial Watershed Projects Annual Report				
✓	Initial Watershed Projects Annual Report 1	100%	04/18/08	04/08/08
✓	Initial Watershed Projects Annual Report 2	100%	06/07/09	06/05/09
✓	Initial Watershed Projects Annual Report 3	100%	06/07/10	06/04/10
✓	Initial Watershed Projects Annual Report 4	100%	06/07/11	06/07/11
✓	Initial Watershed Projects Annual Report 5	100%	06/07/12	06/07/12
✓	Initial Watershed Projects Annual Report 6 (Final Submission)	100%	06/07/13	06/06/13
NMC PROGRAM REQUIREMENTS – 2007 through 2015				
✓	Submit NMC Documentation of Compliance	100%	04/18/08	03/12/08
✓	Complete Additional NMC Compliance Activities (51 Total)	100%	04/18/09	4/18/09 ¹
Submit NMC Annual Report				
✓	NMC Annual Compliance Report 1	100%	09/04/09	05/11/09
✓	NMC Annual Compliance Report 2	100%	09/04/10	06/04/10
✓	NMC Annual Compliance Report 3	100%	09/04/11	06/21/11
✓	NMC Annual Compliance Report 4	100%	09/04/12	07/02/12
✓	NMC Annual Compliance Report 5	100%	09/04/13	09/04/13
✓	NMC Annual Compliance Report 6	100%	09/04/14	09/04/14
✓	NMC Annual Compliance Report 7	100%	09/04/15	09/04/15
	NMC Annual Compliance Report 8	10%	09/04/16	

Consent Decree Compliance Schedule

CONSENT DECREE ACTIVITY		PERCENT COMPLETE	DUE DATE	DATE OF COMPLETION
PUBLIC PARTICIPATION				
✓	Watershed Summit	100%	N/A	08/30/07
✓	Watershed Community Council Meeting 1	100%	N/A	11/27/07
✓	Watershed Community Council Meeting 2	100%	N/A	02/26/08
✓	Watershed Community Council Meeting 3	100%	N/A	05/20/08
✓	Watershed Community Council Meeting 4	100%	N/A	08/19/08
✓	Watershed Community Council Meeting 5	100%	N/A	11/18/08
✓	Watershed Community Council Meeting 6	100%	N/A	02/17/09
✓	Watershed Community Council Meeting 7	100%	N/A	05/20/10
✓	Watershed Community Council Meeting 8	100%	N/A	11/03/10
PUMP STATION OVERFLOW ELIMINATION PLAN (PSOEP) – 2007 through 2015				
✓	Submit PSOEP	100%	10/18/07	09/18/07
Submit PSOEP Annual Report				
✓	PSOEP Annual Report 1	100%	05/14/09	05/11/09
✓	PSOEP Annual Report 2	100%	05/14/10	05/14/10
✓	PSOEP Annual Report 3	100%	05/14/11	05/13/11
✓	PSOEP Annual Report 4	100%	05/14/12	05/14/12
✓	PSOEP Annual Report 5	100%	05/14/13	05/14/13
✓	PSOEP Annual Report 6	100%	05/14/14	05/13/13
✓	PSOEP Annual Report 7	100%	05/14/15	05/14/15
✓	PSOEP Annual Report 8	100%	05/14/16	05/14/16
	PSOEP Annual Report 9	0%	05/14/17	
REPORTING – 2007 through 2015				
Submit Quarterly Report				
✓	Submit Quarterly Report 1	100%	01/30/08	01/30/08
✓	Submit Quarterly Report 2	100%	04/30/08	04/30/08
✓	Submit Quarterly Report 3	100%	07/30/08	07/30/08
✓	Submit Quarterly Report 4	100%	10/30/08	10/30/08
✓	Submit Quarterly Report 5	100%	01/30/09	01/30/09
✓	Submit Quarterly Report 6	100%	04/30/09	04/30/09
✓	Submit Quarterly Report 7	100%	07/30/09	07/30/09
✓	Submit Quarterly Report 8	100%	10/30/09	10/30/09
✓	Submit Quarterly Report 9	100%	01/30/10	01/29/10
✓	Submit Quarterly Report 10	100%	04/30/10	04/30/10
✓	Submit Quarterly Report 11	100%	07/30/10	07/30/10
✓	Submit Quarterly Report 12	100%	10/30/10	10/29/10
✓	Submit Quarterly Report 13	100%	01/30/11	01/28/11
✓	Submit Quarterly Report 14	100%	04/30/11	04/29/11
✓	Submit Quarterly Report 15	100%	07/30/11	07/29/11
✓	Submit Quarterly Report 16	100%	10/30/11	10/28/11
✓	Submit Quarterly Report 17	100%	01/30/12	01/30/12
✓	Submit Quarterly Report 18	100%	04/30/12	04/30/12
✓	Submit Quarterly Report 19	100%	07/30/12	07/30/12
✓	Submit Quarterly Report 20	100%	10/30/12	10/30/12
✓	Submit Quarterly Report 21	100%	01/30/13	01/30/13
✓	Submit Quarterly Report 22	100%	04/30/13	04/30/13
✓	Submit Quarterly Report 23	100%	07/30/13	07/30/13
✓	Submit Quarterly Report 24	100%	10/30/13	10/30/13
✓	Submit Quarterly Report 25	100%	01/30/14	01/30/14
✓	Submit Quarterly Report 26	100%	04/30/14	04/30/14
✓	Submit Quarterly Report 27	100%	07/30/14	07/30/14
✓	Submit Quarterly Report 28	100%	10/30/14	10/30/14
✓	Submit Quarterly Report 29	100%	01/30/15	01/30/15
✓	Submit Quarterly Report 30	100%	04/30/15	04/30/15
✓	Submit Quarterly Report 31	100%	07/30/15	07/30/15
✓	Submit Quarterly Report 32	100%	10/30/15	10/30/15
✓	Submit Quarterly Report 33	100%	01/30/16	01/29/16
✓	Submit Quarterly Report 34	100%	04/30/16	04/30/16
✓	Submit Quarterly Report 35	100%	07/30/16	07/29/16
	Submit Quarterly Report 36	0%	10/30/16	

Consent Decree Compliance Schedule

CONSENT DECREE ACTIVITY		PERCENT COMPLETE	DUE DATE	DATE OF COMPLETION
STATE ENVIRONMENTAL PROJECTS				
✓	Setup 6 Separate Escrow Accounts	100%	10/18/07	10/18/07
✓	Conservancies	100%	04/18/12	04/18/12
✓	Boone County	100%	04/18/12	03/26/12
✓	Campbell County	100%	04/18/12	02/23/12
✓	Kenton County	100%	04/18/12	04/17/12
✓	Licking River Watershed Watch	100%	04/18/12	09/28/11
✓	Split Rock	100%	04/18/12	12/18/08
✓	Education Programs	100%	04/18/12	08/04/11
✓	State Environmental Project Completion Report	100%	06/17/12	06/15/12
SUPPLEMENTAL PROJECTS				
✓	Supplemental Environmental Projects	100%	04/18/12	04/12/12
✓	SEP Completion Reports	100%	06/17/12	06/15/12
WATERSHED PLANS				
Framework for Developing Watershed Plans				
✓	Obtain Public Input on Framework for Watershed Plans	100%	04/09/08	04/09/08
✓	Submit Framework for Watershed Plans	100%	04/18/08	04/17/08
First Round Watershed Plans				
✓	Obtain Public Input on First Round of Watershed Plans	100%	06/27/09	06/08/09
✓	Public Comment Period (5/7/09-6/8/09)	100%	06/08/09	06/08/09
✓	Boone County Public Meeting	100%	N/A	05/14/09
✓	Campbell County Public Meeting	100%	N/A	05/19/09
✓	Kenton County Public Meeting	100%	N/A	05/21/09
✓	Submit First Round of Watershed Plans	100%	06/30/09	06/30/09
✓	Resubmit First Round of Watershed Plans	100%	03/31/11	03/31/11
✓	Resubmit First Round of Watershed Plans - Revision	100%	10/03/13	10/01/13
✓	Final Submission of First Round of Watershed Plans	100%	03/15/14	03/14/14
Second Round Watershed Plans				
	Obtain Public Input on Second Round of Watershed Plans	0%	To Be Determined ²	
	Submit Second Round of Watershed Plans	0%	To Be Determined ²	
Third Round Watershed Plans				
	Obtain Public Input on Third Round of Watershed Plans	0%	To Be Determined ²	
	Submit Third Round of Watershed Plans	0%	To Be Determined ²	
Consent Decree Compliance				
	Consent Decree Compliance - Percentage of Term Complete	51%	12/31/25	

¹ Project schedules for three of the 51 projects were extended beyond 4/18/2009, as described in the 2009 NMC Annual Report. The three projects were complete as of December 2009.

² Deadline is dependent on the approval date of each Watershed Plan.

(This page intentionally left blank for double-sided printing.)

APPENDIX B:
Watershed Improvement Projects

(This page intentionally left blank for double-sided printing.)

Initial Watershed Projects

CIP Title	Basin	Scheduled Completion Date	Actual Completion Date	Status
Initial Watershed Projects				
Strawberry PS Elimination	North	2006	2005	Complete
Beechwood Outfall Sewer Replacement	North	2007	2007	Complete
Eastern Regional - Contract 1--Pond Creek Force Main and Gravity Sewer to Eastern Regional WRF	East	2008	2007	Complete
Eastern Regional - Contract 2--Kahn's Gravity Sewer and Gravity Sewer to the Pond Creek PS	East	2008	2007	Complete
US 27 at Summit Assessment	East	2008	2006	Complete
Eastern Regional - Contract 4--Alex-Licking Gravity Sewer & Force Main to Contract 1	East	2009	2008	Complete
Eastern Regional - Contract 6--Pond Creek PS	East	2008	2007	Complete
Eastern Regional - Contract 8A--Alex-Licking PS	East	2009	2009	Complete
Parkside PS Relocation	East	2008	2007	Complete
Eastern Regional Water Reclamation Facility	East	2008	2008	Complete
Highland Heights PS Study	East	2006	2006	Complete
Wilson/Waterworks Road Relief Sewer Study	East	2008	2007	Complete
Pinehill/Skyview Terrace Sewer	East	2006	2005	Complete
Eastern Regional - Contract 7--Riley Road #2 PS	East	2009	2009	Complete
Eastern Regional - Contract 3--Riley Force Main and Gravity Sewer to the ERWRF	East	2009	2010	Complete
Western Regional - KDOT - Turkeyfoot Road Force Main	West	2006	2005	Complete
Western Regional - Union Sewer (North and South)	West	2013	2008	Complete
American Sign PS Rehabilitation	West	2008	2008	Complete
Allen Fork Collection System - Phase I Improvements	West	2009	2007	Complete
Duncan Drive Assessment Project	West	2007	2006	Complete
Western Regional - Sunnybrook Sewer	West	2013	2010	Complete
Western Regional - Gunpowder Interceptor Sewer	West	2013	2010	Complete
Banklick PS Screening Facility	Central	2006	2005	Complete
Stevenson Road Relief Sewer Project Phase II	Central	2006	2006	Complete
Latonia Combined Sewer Separation	Central	2009	2007	Complete
Licking River Sewer Crossing Study	Central	2007	2007	Complete
McMillan PS Removal	Central	2006	2005	Complete
Meyer Road PS Rehabilitation	Central	2008	2008	Complete
Macke PS Rehabilitation	Central	2008	2008	Complete

Initial Watershed Projects

CIP Title	Basin	Scheduled Completion Date	Actual Completion Date	Status
Initial Watershed Projects				
Richwood PS Improvements	Central	2006	2005	Complete
Patton Street Sewer Study	Central	2006	2006	Complete
South Hills Outfall	Central	2008	2007	Complete
Grit Chamber Projects	Multiple	2010	2008	Complete
Fort Wright Illicit Discharge Removal	Multiple	2007	2006	Complete
Fort Wright Sanitary Sewer Rehabilitation Phase 1	Multiple	2007	2006	Complete
Fort Wright Outfall Sewer - Phase II	Multiple	2006	2006	Complete
Dry Creek Treatment Plant - Grit Removal Modifications	Multiple	2006	2005	Complete
Large Diameter Sewer Assessment Program - Phase III	Multiple	2007	2006	Complete
Brookwood Subdivision SSES Study	Multiple	2006	2006	Complete
Southern Kenton Drainage Study	Multiple	2007	2006	Complete
Wilson Road Sewer Assessment Project	Multiple	2006	2005	Complete
Apple Drive Sewer Outfall	Multiple	2006	2006	Complete
Bluegrass Swim Club Sewer Separation	Multiple	2008	2007	Complete
Eastern Regional – Sunset Pump Station and Force Main Improvements	East	2010	2010	Complete
Western Regional Conveyance System to Western Regional WRF	West	2013	2012	Complete
Western Regional Water Reclamation Facility	West	2013	2012	Complete
Western Regional - Narrows Road Diversion PS	West	2013	2012	Complete
Western Regional - Frogtown Interceptor Sewer (from Sunnybrook Dr. to Frogtown Rd.)	West	2014	2012	Complete
Western Regional - South Fork Gunpowder Interceptor Sewer and Rosetta Sewer	West	2013	2012	Complete
Western Regional - Turkeyfoot Industrial Road Force Main	West	2013	2012	Complete
Western Regional - Richwood Sewer and Force Main	West	Removed from Initial Watershed Projects. Approved in letter from Cabinet dated May 13, 2013.		

Watershed Plan Projects: Five Year Program

System-wide Programs

CIP Title	Basin	Project Description	Target Project Benefit	Scheduled Completion Date	Actual Completion Date	Past Activity for 04/01/2016 to 06/30/2016	Planned Activity for 07/01/2016 to 09/30/2016
Priority Inflow and Infiltration Source Identification & Removal Program							
Lakeview I/I Source Identification & Removal	Central	SSES activities and I/I removal in areas where found to be cost effective and feasible upstream of the Lakeview Pump Station	Reduce I/I and SSOs in Lakeview PS service area	Beyond 2016	n/a	Flow Monitoring and Initial Design	Flow Monitoring and Initial Design
Licking River Siphon Source Identification and Removal	Central	SSES activities and I/I removal in areas where found to be cost effective and feasible upstream of the Licking River Siphon	Reduce I/I and SSOs in Licking River Siphon area	Beyond 2016	n/a	Initial Design	Initial Design
Taylor Creek Source Identification and Removal	East	SSES activities and I/I removal in areas where found to be cost effective and feasible in the Taylor Creek area	Reduce I/I and SSOs in Taylor Creek area	Beyond 2016	n/a	Initial Design	Initial Design
Green Programs (DRIP & GrIPP)							
Boone Woods YMCA Detention Model	North	Partnership with Northern Kentucky University Center for Applied Ecology to retrofit a detention basin on Boone Woods YMCA property	Improve Water Quality	2010	2010	Complete	
City of Covington: 12th Street Bioswale	North	Partnership with City of Covington to install street planters leading to a bioswale and rain garden along 12th Street	Reduce CSO volume	2011	2011	Complete	
City of Covington: Main Strasse Gateway Biofiltration Swale	North	Partnership with City of Covington and Transit Authority of Northern Kentucky to install biofiltration swales on city property at the Bakewell parking lot	Reduce CSO volume	2012	2013	Complete	
Notre Dame Academy Basin Retrofit	North	Partnership with Notre Dame Academy to retrofit an existing detention basin on school property	Reduce CSO volume	2009	2009	Complete	
City of Ft. Thomas: Rossford Park Rain Garden	East	Partnership with City of Ft. Thomas to install rain gardens at Rossford Park	Improve Water Quality	2012	2012	Complete	
City of Ft. Thomas: Memorial Parkway Bioswale	East	Partnership with City of Ft. Thomas to install a bioswale at the Northern Kentucky Water District property located along Memorial Parkway.	Improve Water Quality	2010	2010	Complete	
Kenton County School District: Turkeyfoot Middle School	Central	Partnership with Kenton County School District to install rain garden at Turkeyfoot Middle School	Improve Water Quality	2010	2010	Complete	
City of Covington: Madison Ave. Rain Garden	North	Partnership with City of Covington to install two rain gardens or street planters within the right-of-way along Madison Avenue	Reduce CSO volume	2013	2013	Complete	
Kenton County Public Library: Mary Ann Morgan Branch	North	Partnership with Kenton County Library to install rain gardens and permeable pavers on site at the Mary Ann Morgan Branch	Reduce CSO volume	2013	2013	Complete	
Demonstration Projects (Pilot Projects & Innovative Technology Testing)							
St. Elizabeth Detention Basin Retrofit	North	Modification of an existing dry detention basin located on property owned by St. Elizabeth Medical Center.	Reduce CSO volume in the Willow Run Sewershed	2009	2009	Complete Post-Construction Monitoring	
Prisoner's Lake Rainwater Harvesting	North	Construction of a small storm water pumping station and force main to capture storm water runoff from Prisoner's Lake that will be re-used in an irrigation pond for a small public golf course.	Manage storm water entering the CSS	2010	2010	Complete	
Terraced Reforestation	North	Construction of a series of vegetated, terraced berms within the I-71/75 right-of-way in the City of Covington.	Manage storm water entering the CSS	2010	2011	Complete Post-Construction Monitoring	
Watershed Controls Pilot Projects - Regional and Decentralized Controls							
Regional Project: Banklick Regional Wetlands	Central	Constructed wetland that treats flow diverted from Banklick Creek to reduce bacteria concentrations.	Improve water quality of Banklick Creek	2011	2011	Complete Post-Construction Monitoring	
Decentralized Control Project	Central	Storm water control measures such as wetlands, biofiltration basins, and enhanced retention serving upstream drainage areas smaller than one square mile, but typically greater than five acres	Improve water quality of local streams	Beyond 2016	n/a	Initial Design	Initial Design

Watershed Plan Projects: Five Year Program

Specific Basin Projects

CIP Title	Basin	Project Description	Target Project Benefit	Scheduled Completion Date	Actual Completion Date	Past Activity for 04/01/2016 to 06/30/2016	Planned Activity for 07/01/2016 to 09/30/2016
<i>(Schedules listed in this section are subject to change based on the approval of SD1's Watershed Plans.)</i>							
Van Deren Sanitary Sewer Improvements	North	Sanitary and storm sewer improvements in a 100 home area to separate common manholes and remove illicit connections and I/I	Reduce SSOs and illicit discharges in Lakeside Park	2011	2011	Complete	
Avon Drive Sanitary Sewer Improvements	North	Replacement of 570 LF of 12-inch sewer with 24-inch pipe and installation of new storm sewer	Reduce SSOs in Lakeside Park	2010	2010	Complete	
Willow Run Direct Entry Point Bar Racks	North	Installed bar racks on 10 direct entry points where open storm channels discharge into sewer system	Reduce debris entry into system, maintain capacity and reduce blockages	2009	2010	Complete	
KYTC Basin - Green Infrastructure Retrofit	North	Conversion of traditional detention basin near I-75 to provide greater detention and infiltration by modifying the outlet structure and other improvements	CSO reduction, informs future green infrastructure design	2012	2011	Complete Post-Construction Monitoring	
Lakeview PS Pump Replacement	Central	Replacement of 8 pumps at the Lakeview pump station along with piping and electrical improvements to provide a reliable peak capacity of 22.5 MGD	Reduce SSOs at Lakeview PS and increase PS reliability	2014	2013	Complete	
Church Street (gray, green, and watershed controls)	Central	The separation of street load on six streets, new biofiltration basin and installation of approximately 1,300 linear feet of new 72-inch sewer.	Reduce CSO frequency and volume into Banklick Creek and improve structural integrity of sewer infrastructure.	2014	Ph 1 - 2015	Ph 1 - Complete Post-Construction Monitoring	
					Ph 2 - n/a	Ph 2 - Construction	Ph 2 - Construction
Vernon Lane – Public & Private Source I/I Removal	Central	Combination of private I/I removal, sewer rehabilitation, manhole lining, and stormwater BMPs in area comprising approximately 270 homes	Eliminate Vernon Ln. SSO and improve water quality	Beyond 2016	Ph 1 - 2014	Ph 1 - Complete Post-Construction Monitoring	
					Ph 2 - n/a	Ph 2 - Construction	Ph 2 - Construction
Ash Street PS and Forcemain	East	Construction of a new approximately 7 MGD pump station in Silver Grove and new force main to the Riley Rd. Pump Station in Alexandria. Also includes new force main to redirect flow from the Silver Grove PS to the Ash St. PS	Reduce overflows from Silver Grove CSO and SSO reduction in the Highland Heights PS and Silver Grove PS service areas.	2017	n/a	Final Design	Final Design
Riviera Sewer Replacement	East	Replacement of approximately 4,100 LF of deteriorated 24-inch pipe in the Taylor Creek area	Reduce CSOs into Taylor Creek and address structural issues	Beyond 2016	n/a	Initial Design	Initial Design
		Emergency repair of approximately 1,300 LF of collapsed 24-inch pipe. Upsize to 54-inch pipe.	Replace collapsed inceptor and provide additional capacity.	2016	2016	Complete	Complete Post-Construction Monitoring
Lakeside Park – Public Sewer Rehab and Private Source Removal	North	Combination of private I/I removal, sewer rehabilitation/replacement and manhole lining, and stormwater BMPs where feasible in Lakeside Park	Eliminate SSOs in Lakeside Park	Beyond 2016	Ph 1 - 2014	Ph 1 - Complete	
					Ph 2 - n/a	Ph 2 - In Progress	Ph 2 - In Progress
Willow Run Dynamic Control Facility	North	Construction of a dynamic weir facility at the Willow Run overflow diversion to provide in-line storage	CSO reduction using in-line storage	Beyond 2016	n/a	Initial Design	Initial Design

Other Committed Projects

CIP Title	Basin	Project Description	Target Project Benefit	Scheduled Completion Date	Actual Completion Date	Past Activity for 04/01/2016 to 06/30/2016	Planned Activity for 07/01/2016 to 09/30/2016
<i>(Schedules listed in this section are subject to change based on the approval of SD1's Watershed Plans.)</i>							
Donnemeyer Improvements, Newport Pavilion Improvements, Bellevue Relief Sewer, Wilson/Waterworks Road, Covert Run	East	Multiple sewer projects including replacement with larger 18-30 -inch diameter sewers in the Taylor Creek area. Also included private source I/I removal	Reduce CSO and SSO in Taylor Creek area and address basement flooding	2011	2011	Complete	
Dry Creek WWTP Headworks Improvements	North	Construction of a new 110 MGD headworks facility at the Dry Creek WWTP	Increase reliability and wet weather treatment capacity at Dry Creek WWTP	2013	2013	Complete	

Additional CSO and SSO Reduction Projects

Project Title	Basin	Project Description	Target Project Benefit	Scheduled Completion Date	Actual Completion Date	Planned Activity for FY 2016
CSO Reduction						
Aqua on the Levee	East	In partnership with a developer to construct a 48" separate storm outfall through the Ohio River levee in Newport. Project will provide storm water offloading opportunity for 5 acres, and extended opportunity for 19 acres of additional offloading along Saratoga St. Maximum extent of offloading opportunity with new storm outfall will be 38 acres, including Washington St.	Reduce CSO volumes at Saratoga St and Washington St CSOs approximately 4 MG in typical year with proximal separation. Extended separation will provide approximately 7.5 MG reduction in typical year. The maximum extent separation will provide more than 17 MG of CSO reduction during the typical year.	2016	N/A	Permitting & Construction
Catch Basin Retrofits C480-11	Central & North	Strategically disconnect catch basins in the CSS that are tied into the collection lines, main interceptors, or the regulating diversion MHs. Reconnect the catch basins to the wet-weather CSO outfall line, effectively removing the inflows from the CSS mainlines. Retrofit all reconnected CBs with solids and floatable controls.	Partial removal of street inflows in various areas of the combined system: Kenner St (Ludlow) = 2 CBs Adams St + Eastern Ave (Covington) = 3 CBs Garrard St + Riverside Dr (Covington) = 4 CBs Greenup St + Riverside Dr (Covington) = 2 CBs Pike St + Rohmann Ave (Covington) = 4 CBs Virginia Ave + 45th St (Covington) = 2 CBs Warren St (Covington) = 3 CBs	2011	2011	Complete
Covington Detention Basins	North	In partnership with the City of Covington, construct detention basins in the low lying areas of the Peasleburg neighborhood to mitigate flooding from peak storm events.	The detention basins will provide approximately 2.5 to 3.5 MG of typical year CSO reduction in the Willow Run system.	2015	2015	Complete
Hazen Street, Ludlow Separation	North	In partnership with the City of Ludlow, replace and reconfigure CSS catch basins to improve drainage.	Consolidates CSS catch basins on Hazen St and at the entrance of River's Breeze Condominiums. Extends the initial scope of disconnection in Ludlow, beyond what was identified in Figure 8.2a of the Watershed Plans. Full disconnection will be possible with a new 42" separate storm pipe on West St.	2013	2013	Complete
Jacob Price Ph1	Central	Stormwater offloading from approximately 7.5 acres of Covington Housing development	Reduce CSO approximately 5.5 million gallons at Robbins St and 11th St.	2014	2014	Complete
Jacob Price Ph3	Central	Additional stormwater offloading of 9 acres adjacent to Jacob Price Ph 1 redevelopment, including installation of BMP for WQ..	CSO reduction at 9th St and 10th St.	Beyond 2017	N/A	Initial Design
Park Hills Separation	North	In partnership with the City of Park Hills, replace and locally separate CSS catch basins to improve drainage. Streets improved: Alhambra Ct, Exter Dr, Coram St, Harriet St, Irishrose Ln, Old State Rd, South Arlington Rd.	Removes catch basins from the local CSS and redirects to a drainage ditch. The ditch drains to Willow Run CSS, further downstream. This localized separation provides opportunity to completely remove the identified street flows from the Willow Run CSS with the replacement of the Brent Spence Bridge.	2015	2015	Complete

Additional CSO and SSO Reduction Projects

Project Title	Basin	Project Description	Target Project Benefit	Scheduled Completion Date	Actual Completion Date	Planned Activity for FY 2016
State Route KY9 Realignment	Central	In partnership with KY Transportation Cabinet, offload stormwater from the existing CSS on approximately 2.5 miles of newly realigned state route KY9, along the Licking River in Newport. KYTC's proposed 36" separate storm pipe will be upsized by SD1 to 60" to accommodate additional offloading in the future. Utilizes two existing CSO outfalls and requires the construction of one new separate storm outfall through the levee.	Reduces CSO volumes in the short term at 4th St, 9th St, 10th St, and 12 St CSOs by approximately 10 MG. Maximum extent of potential separation in Newport is approximately 167 acres with the new separate storm outfall, which will provide approximately 63 MG of CSO reduction. Project also rehabilitates all intersecting sanitary assets and eliminates discovered illicit connections to the CSO outfalls.	2016	N/A	Construction
Victory Ave Storm Sewer Improvement	Central	Construct a new 15" separate storm sewer to alleviate flooding of private property in south Covington.	Allows disconnection of four existing CSS catch basins that collect approximately 0.3 acres of street runoff. Reduces combined flows tributary to the Banklick PS and offloads to the Banklick Creek.	2016	N/A	Design & Construction
Water's Edge	East	Construct a new 36" separate storm sewer and disconnect existing CSS catch basins on Taylor Ave in Bellevue. Integrate BMPs for WQ. Four phases of offloading.	Reduce CSO volumes at Taylor Ave CSO and other local CSOs by approximately 6.1 MG in the typical year with Ph 1 and 15.68 MG with Ph 4. Improves flooding issues on Taylor and Eden Avenues.	2017	N/A	Design & Construction
SSO Reduction						
Richwood Forcemain Reroute	West	Remove Richwood PS from the Dry Creek/Lakeview PS sewershed and reroute to Western Regional Water Reclamation Facility with a new 20" force main.	Reduces SSO volume in the 2 year 6 hour event by approximately 1.4 MG, and eliminates six Recurring and Inactive SSOs.	2016	N/A	Design & Construction
43rd St and Decoursey Ave	Central	Evaluate and improve hydraulics in existing 18" main in south Covington.	Eliminate recurring basement backups in approximately 10 homes.	Beyond 2016	N/A	Initial Design
Demonstration Projects (Pilot Projects & Innovative Technology Testing)						
Injection Wells Pilot	North, Central, East	Disconnect catch basins in portions of the CSS in Ludlow, Covington, and Bellevue for deep well injection into the alluvium, in three pilot areas.	Reduce activations and volumes at the Adella St CSO (Ludlow), E 6th St CSO (Covington), and Patchen St CSO (Bellevue)	Beyond 2016	N/A	Drill monitoring wells to determine WQ and infiltration rates. Permitting.

Pump Station Backup Power Plan

CIP Title	Basin	Original Proposed Solution	Updated Solution	Scheduled Completion Date	Actual Completion Date	Final Status as of October 2015
Category 1 Projects (4 total projects)						
Alex Licking	East	Permanent Generator	n/a	2008	2008	Complete
American Sign	West	Permanent Generator	n/a	2008	2008	Complete
Riley Road	East	Permanent Generator	n/a	2009	2009	Complete
Sunset	East	Permanent Generator	Backup Dry Prime Pump with a Diesel	2010	2010	Complete
CIP Title	Basin	Original Proposed Solution	Updated Solution	Scheduled Completion Date	Actual Completion Date	Final Status as of October 2015
Category 2 Projects (21 total projects)						
Kahns	East	PS Elimination	n/a	2007	2007	Complete
Meadow Hill	Central	PS Elimination Study	PS Elimination	Study - 2008 2012 - 2015	2008 2010	Complete
Riley Road No. 1	East	PS Elimination	n/a	2009	2009	Complete
Riley Road No. 2						
Riverwatch PS	North	PS Elimination Study	PS Elimination	Study - 2008 2012 - 2015	2008 2008	Complete
South Park Industrial	North	PS Elimination Study	Backup Dry Prime Pump with a Diesel	Study - 2008 2012 - 2015	2008 2010	Complete
Wedgewood Dr	Central	PS Elimination Study	Electrical hook up for portable generator	Study - 2008 2015	2008 2015	Complete
Willow Bend No. 2	West	PS Elimination Study	PS Elimination	Study - 2008 2013	2008 2013	Complete
Army Reserve	East	PS Elimination Study	Electrical hook up for portable generator	Study - 2008 2013-2014	2008 2014	Complete
Eagles Landing	West	PS Elimination Study	Electrical hook up for portable generator	Study - 2008 2013-2014	2008 2014	Complete
Evergreen	Central	PS Elimination Study	Electrical hook up for portable generator	Study - 2008 2014	2008 2014	Complete
Lamphill	East	PS Elimination Study	Electrical hook up for portable generator	Study - 2008 2011	2008 2011	Complete
Mill House Crossing	Central	PS Elimination Study	Backup Dry Prime Pump with a Diesel	Study - 2008 2012	2008 2012	Complete
Ridgefield	North	PS Elimination Study	Backup Dry Prime Pump with a Diesel	Study - 2008 2014	2008 2014	Complete
War Admiral	West	PS Elimination Study	PS Elimination	Study - 2008 2012 - 2015	2008 2011	Complete
Blackstone	West	PS Elimination Study	Electrical hook up for portable generator	Study - 2008 2015	2008 2015	Complete
Dublin Green No. 1	West	PS Elimination Study	PS Elimination	Study - 2008 2015	2008 2012	Complete
Fowler Creek	West	PS Elimination	These stations were eliminated after the Western Regional collection system became operational.	2013	2011	Complete
Gammon Calmet	West	PS Elimination		2013	2012	Complete
Gunpowder	West	PS Elimination		2013	2012	Complete
Union	West	PS Elimination		2013	2012	Complete

Pump Station Backup Power Plan

CIP Title	Basin	Original Proposed Solution	Updated Solution	Scheduled Completion Date	Actual Completion Date	Final Status as of October 2015
Category 3 Projects (24 total projects)						
Airport Exchange Ind Park	North	Permanent Generator	n/a	2009	2009	Complete
Barrs Branch	East	Permanent Generator	Portable Generator	2009	2009	Complete
Cedar Point	East	Permanent Generator	n/a	2009	2009	Complete
Bullitsville	North	Permanent Generator	n/a	2008	2008	Complete
Catalpa	Central	Permanent Generator	n/a	2009	2009	Complete
Centerplex	East	Permanent Generator	n/a	2008	2008	Complete
Hempsteade	West	Permanent Generator	n/a	2009	2009	Complete
Highland Heights	East	Portable Generator	n/a	2009	2009	Complete
Dublin Green No. 2	West	Permanent Generator	n/a	2009	2009	Complete
Brookwood	East	Permanent Generator	n/a	2009	2009	Complete
Ky Aire	West	Permanent Generator	n/a	2008	2007	Complete
Levi	West	Permanent Generator	n/a	2008	2007	Complete
Maple Ave	Central	Permanent Generator	n/a	2009	2009	Complete
Sand Run	North	Permanent Generator	n/a	2008	2008	Complete
Saturn	West	Permanent Generator	n/a	2009	2009	Complete
Second Street	Central	Permanent Generator	n/a	2009	2009	Complete
Skyport	North	Permanent Generator	n/a	2008	2008	Complete
South Hampton	West	Permanent Generator	n/a	2008	2007	Complete
Thornwilde	North	Permanent Generator	n/a	2008	2008	Complete
Bunning Lane	East	PS Elimination Study	Electrical hook up for portable generator	2015	2015	Complete
Kees	East	Permanent Generator	Backup Dry Prime Pump with a Diesel	2011	2011	Complete
Overlook	East	Permanent Generator	Electrical hook up for portable generator	2015	2015	Complete
Riverview Farms	North	Permanent Generator	Electrical hook up for portable generator	2015	2015	Complete
Stillwater	East	Permanent Generator	Electrical hook up for portable generator	2015	2015	Complete

Pump Station Backup Power Plan

CIP Title	Basin	Original Proposed Solution	Updated Solution	Scheduled Completion Date	Actual Completion Date	Final Status as of October 2015
Category 4 Projects (50 total projects)						
Banklick	Central	Permanent Generator	n/a	2009-2014	2009	Complete
Cedar	Central	Permanent Generator	n/a	2009-2014	2009	Complete
Fowler Ridge	Central	Permanent Generator	Backup Dry Prime Pump with a Diesel	2009-2014	2010	Complete
Lassing Green	West	Permanent Generator	n/a	2009-2014	2009	Complete
Leathers Rd	Central	Permanent Generator	Backup Dry Prime Pump with a Diesel	2009-2014	2010	Complete
Marshall Rd	Central	Permanent Generator	n/a	2009-2014	2010	Complete
Mineola Pike	North	Permanent Generator	Backup Dry Prime Pump with a Diesel	2009-2014	2010	Complete
Newport Steel Mill	East	Permanent Generator	n/a	2009-2014	2009	Complete
Paul Rd	East	Permanent Generator	Portable Generator	2009-2014	2010	Complete
Rosewood Lane	East	Permanent Generator	Backup Dry Prime Pump with a Diesel	2009-2014	2010	Complete
Shadow Lake	East	Permanent Generator	Backup Dry Prime Pump with a Diesel	2009-2014	2009	Complete
Wolf Rd	Central	Permanent Generator	Backup Dry Prime Pump with a Diesel	2009-2014	2009	Complete
Air Park West	North	Permanent Generator	Backup Dry Prime Pump with a Diesel	2009-2014	2011	Complete
Arbortech	North	Permanent Generator	Backup Dry Prime Pump with a Diesel	2012	2012	Complete
Arborwood	North	Permanent Generator	Backup Dry Prime Pump with a Diesel	2014	2014	Complete
Brandtly Ridge	Central	Permanent Generator	Backup Dry Prime Pump with a Diesel	2012	2012	Complete
Brentwood	North	Permanent Generator	Electrical hook up for portable generator	2015	2014	Complete
Brushup Lane	West	Permanent Generator	PS Elimination	2012	2012	Complete
Carlisle Ave	East	Permanent Generator	Backup Dry Prime Pump with a Diesel	2014	2014	Complete
Cinnamon Ridge	West	Permanent Generator	Backup Dry Prime Pump with a Diesel	2012	2012	Complete
Cold Spring Crossing	East	Permanent Generator	Permanent Generator	2014	2014	Complete
Cold Spring Plaza	East	Permanent Generator	Backup Dry Prime Pump with a Diesel	2012	2012	Complete
Darma Ct	East	Permanent Generator	Electrical hook up for portable generator	2013-2014	2014	Complete
Deer Creek No. 1	North	Permanent Generator	Backup Dry Prime Pump with a Diesel	2009-2014	2011	Complete
Deer Creek No. 2	North	Permanent Generator	Backup Dry Prime Pump with a Diesel	2009-2014	2011	Complete
Eighth Street	Central	Connect to Grid Power	Permanent Generator	2015	2015	Complete
Gerrard Ave	East	Permanent Generator	Portable Generator	2009-2014	2011	Complete
Golf Course	Central	Permanent Generator	Electrical hook up for portable generator	2012	2012	Complete
Hampton Ridge	West	Permanent Generator	Electrical hook up for portable generator	2015	2015	Complete
Harrison Harbor	East	Permanent Generator	Portable Generator	2009-2014	2011	Complete

Pump Station Backup Power Plan

CIP Title	Basin	Original Proposed Solution	Updated Solution	Scheduled Completion Date	Actual Completion Date	Final Status as of October 2015
Category 4 Projects (continued)						
Harvest Hill	Central	Permanent Generator	Backup Dry Prime Pump with a Diesel	2014	2014	Complete
ICH	Central	Permanent Generator	Electrical hook up for portable generator	2011	2011	Complete
IDI	North	Permanent Generator	Electrical hook up for portable generator	2012	2012	Complete
Independence Station Rd	Central	Permanent Generator	Backup Dry Prime Pump with a Diesel	2009-2014	2011	Complete
Jefferson Ave	East	Permanent Generator	Portable Generator	2009-2014	2011	Complete
Jericho Rd	Central	Permanent Generator	Electrical hook up for portable generator	2011	2011	Complete
Jonathan	West	Permanent Generator	Electrical hook up for portable generator	2015	2015	Complete
Litton	North	Permanent Generator	Electrical hook up for portable generator	2012	2012	Complete
Ohio Ave	East	Permanent Generator	Portable Generator	2009-2014	2011	Complete
Orchard Estates	West	Permanent Generator	Backup Dry Prime Pump with a Diesel	2014	2014	Complete
Parkside No. 2	East	Permanent Generator	Electrical hook up for portable generator	2012	2012	Complete
Patton Street	Central	Dual Utility Power Feed	Permanent Generator	2015	2014	Complete
Ria Vista	North	Permanent Generator	Electrical hook up for portable generator	2011	2011	Complete
Silver Grove	East	Permanent Generator	Permanent Generator	2015	2015	Complete
St Annes	East	Permanent Generator	Backup Dry Prime Pump with a Diesel	2014	2014	Complete
Sycamore	West	Permanent Generator	PS Elimination	2015	2012	Complete
Taylor Mill Rd	Central	Permanent Generator	Electrical hook up for portable generator	2011	2011	Complete
Wilder	East	Permanent Generator	Backup Dry Prime Pump with a Diesel	2014	2014	Complete
Wyndemere	North	Permanent Generator	Electrical hook up for portable generator	2012	2012	Complete
Youell Rd	West	Permanent Generator	Electrical hook up for portable generator	2012	2012	Complete

Pump Station Backup Power Plan

CIP Title	Basin	Original Proposed Solution	Updated Solution	Scheduled Completion Date	Actual Completion Date	Final Status as of October 2015
Category 5 Projects (6 total projects)						
Keavy	Central	Permanent Generator	Backup Dry Prime Pump with a Diesel	2010-2015	2010	Complete
Meadow Lane	Central	Permanent Generator	Backup Dry Prime Pump with a Diesel	2010-2015	2009	Complete
Cardinal Cove	North	Permanent Generator	Permanent Generator	2015	2013	Complete
Crestview	East	Permanent Generator	Backup Dry Prime Pump with a Diesel	2015	2015	Complete
Ripple Creek	East	PS Elimination Study	PS Elimination	2010-2015	2010	Complete
Winters Lane No. 2	East	Permanent Generator	Electrical hook up for portable generator	2014	2014	Complete
CIP Title	Basin	Original Proposed Solution	Updated Solution	Scheduled Completion Date	Actual Completion Date	Final Status as of October 2015
Category 6 Projects (5 total projects)						
Enzweiller	East	Permanent Generator	n/a	2012-2015	2009	Complete
Mafred	Central	Permanent Generator	Backup Dry Prime Pump with a Diesel	2012-2015	2009	Complete
Ridgeway	Central	Permanent Generator	Backup Dry Prime Pump with a Diesel	2012-2015	2009	Complete
Richwood	West	Permanent Generator	Backup Dry Prime Pump with a Diesel	2012	2012	Complete
Twin Lakes	Central	Permanent Generator	Backup Dry Prime Pump with a Diesel	2014	2014	Complete

Progress Summary	Number
2007 Complete Projects	4
2008 Complete Projects	8
2009 Complete Projects	24
2010 Complete Projects	11
2011 Complete Projects	16
2012 Complete Projects	18
2013 Complete Projects	2
2014 Complete Projects	16
2015 Complete Projects	11
Total Complete	110

Pump Station Overflow Elimination Plan

CIP Title	Basin	Scheduled Completion Date	Actual Completion Date	Activity for 04/01/2016 to 06/30/2016	Planned Activity for 07/01/2016 to 09/30/2016
Pump Station Overflow Elimination Projects					
Alex-Licking	East	12/31/2010	2008	Complete	Complete
Allen Fork	North	12/31/2015	2014	Complete	Complete
Crestview	East	12/31/2015	2015	Complete	Complete
Harrison Harbor	East	12/31/2010	*See PS Overflow Elimination Annual Report May 11, 2009	Complete	Complete
Highland Acres	West	12/31/2010	2010	Complete	Complete
Kentucky Aire	West	12/31/2013	2014	Complete	Complete
Riley Road No.1	East	12/31/2010	2009	Complete	Complete
Ripple Creek	Central	12/31/2010	2010	Complete	Complete
South Hampton	West	3/31/2013	2012	Complete	Complete
South Park	North	12/31/2010	2010	Complete	Complete
Sunset	Central	12/31/2010	2010	Complete	Complete
TaylorSPORT	North	12/31/2010	2004	Complete	Complete
Union	West	3/31/2013	2012	Complete	Complete
Lakeview	Central	12/31/2023 ¹	n/a	In-Progress	In-Progress


¹ Revised deadline approved in letter from Cabinet dated May 13, 2013.

APPENDIX C:
Cumulative and Annual Overflow Data


(This page intentionally left blank for double-sided printing.)

**Cumulative Overflow Data
January 1, 2016 through June 30, 2016**


Rainfall

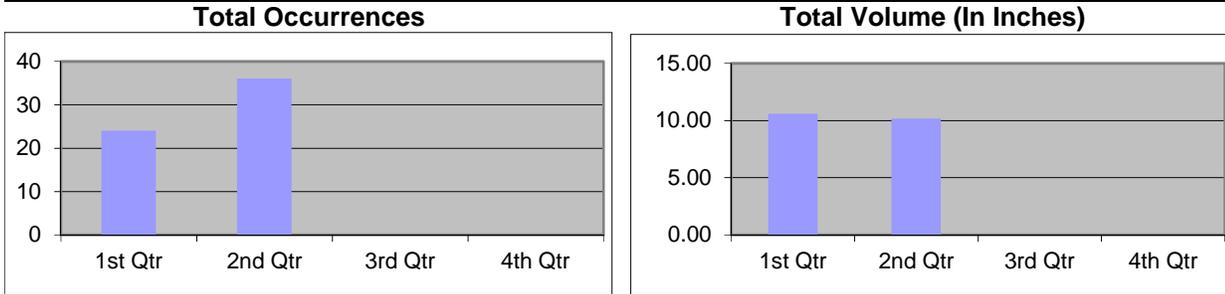


SSOs - Due to Wet Weather (WW) and Operational Issues

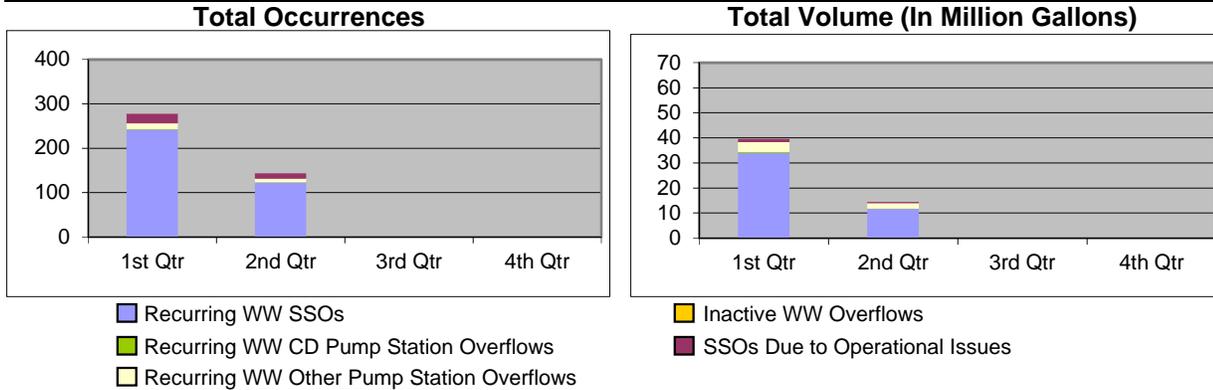


Dry Weather CSOs

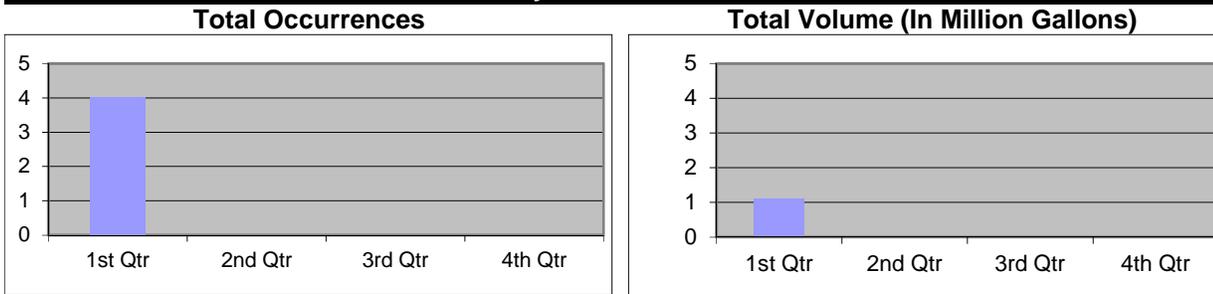

Wet Weather CSOs

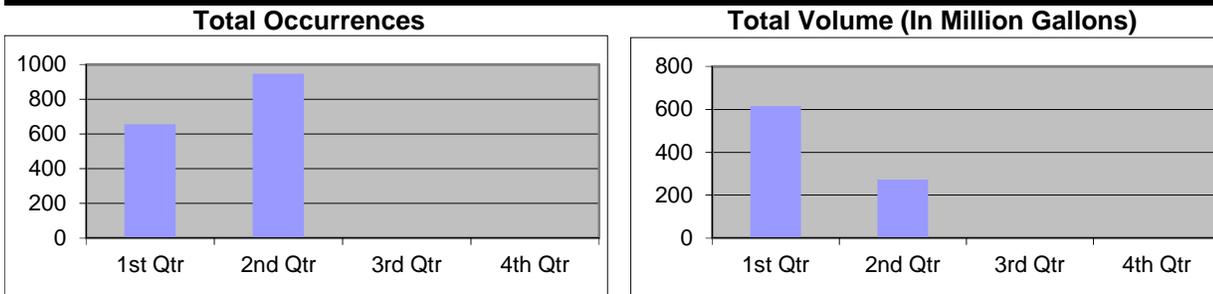

Building Backups

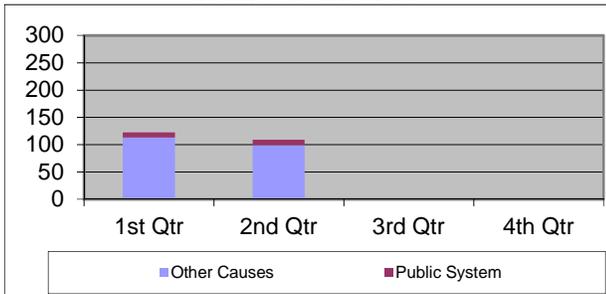


2016 Overflow Summary

	Occurrences	Volume
Rainfall	60	20.720 inches
Recurring WW SSOs	387	52.122 MG
Inactive WW SSOs	0	0.000 MG
Operational SSOs	33	1.757 MG
Dry Weather CSOs	4	1.089 MG
Wet Weather CSOs	1601	885.080 MG
Building Backups (Other Causes)	212	
Building Backups (Public System)	19	


Annual Cumulative Overflow Data 2008 through 2016Q2

Rainfall

Total Occurrences

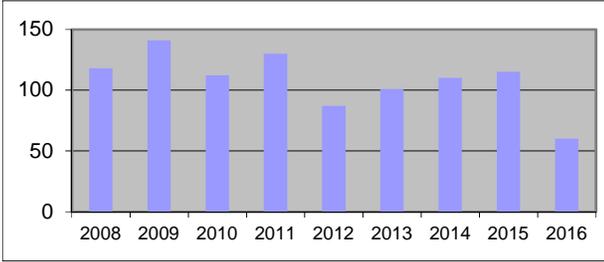


Total Volume (In Inches)

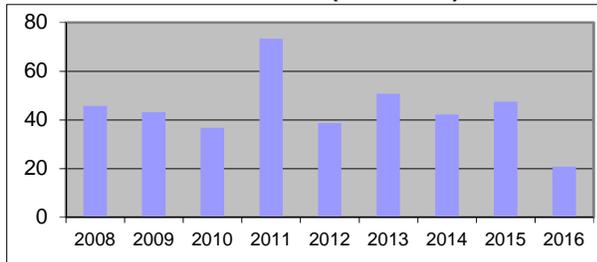


SSOs - Due to Wet Weather (WW) and Operational Issues

Total Occurrences

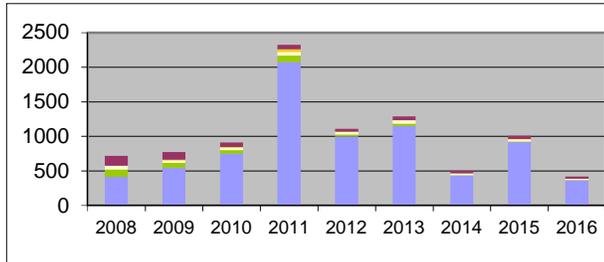


Total Volume (In Million Gallons)

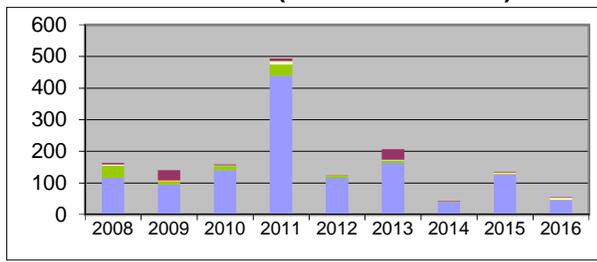


- Recurring WW SSOs
- Inactive WW Overflows
- Recurring WW CD Pump Station Overflows
- SSOs Due to Operational Issues
- Recurring WW Other Pump Station Overflows

Dry Weather CSOs

Total Occurrences

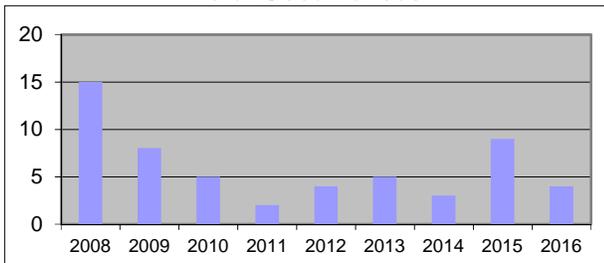


Total Volume (In Million Gallons)

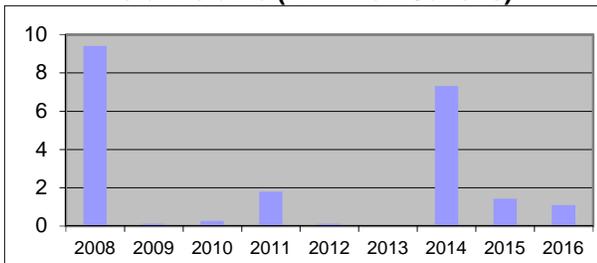


Wet Weather CSOs

Total Occurrences

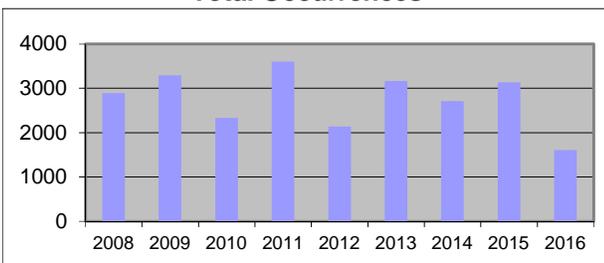


Total Volume (In Million Gallons)

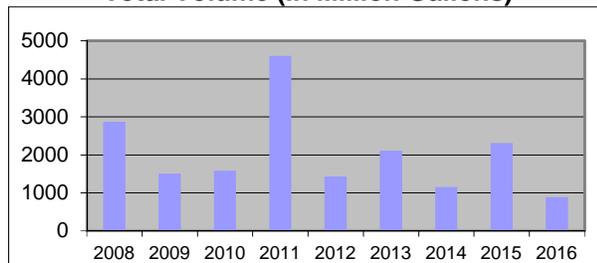

Building Backups

Total Occurrences

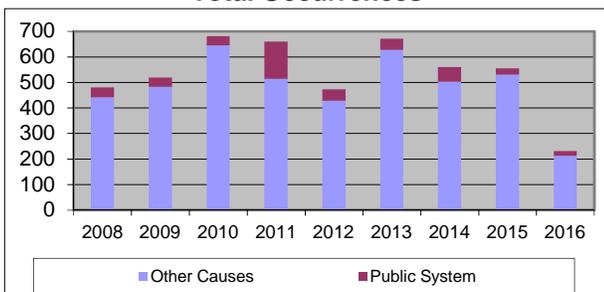

Change from 2015 to 2016Q2

	Occurrences	Volume	
Rainfall	-55	-26.66	inches
Recurring WW SSOs	-571	-78.354	MG
Inactive WW SSOs	-3	-2.118	MG
Operational SSOs	-11	-0.277	MG
Dry Weather CSOs	-5	-0.327	MG
Wet Weather CSOs	-1533	-1424.48	MG
Building Backups (Other Causes)	-318		
Building Backups (Public System)	-6		

APPENDIX D:
Recurring Wet Weather SSOs

(This page intentionally left blank for double-sided printing.)

Recurring Wet Weather SSOs

No.	MHID	City	County	Model Predicted Overflow Activations	Model Predicted Overflow Volume (MG)
1	0020006	Silver Grove	Campbell	5	0.96
2	0020007	Silver Grove	Campbell	4	0.07
3	0020008	Unicorp Campbell County	Campbell	4	0.05
4	0020030	Silver Grove	Campbell	0	0.00
5	0020032	Unicorp Campbell County	Campbell	1	0.08
6	0040003	Fort Thomas	Campbell	0	0.00
7	0050022	Fort Thomas	Campbell	0	0.00
8	0060001	Unicorp Campbell County	Campbell	2	0.02
9	0060002	Unicorp Campbell County	Campbell	2	0.00
10	0060004	Unicorp Campbell County	Campbell	2	0.03
11	0110010	Highland Heights	Campbell	1	0.01
12	0120018	Highland Heights	Campbell	0	0.00
13	0120019	Highland Heights	Campbell	0	0.00
14	0150003	Wilder	Campbell	0	0.00
15	0150005	Wilder	Campbell	0	0.00
16	0150009	Wilder	Campbell	2	0.08
17	0150063	Wilder	Campbell	4	0.01
18	0150064	Wilder	Campbell	4	0.25
19	0150065	Wilder	Campbell	4	0.09
20	0150356	Southgate	Campbell	0	0.00
21	0150399	Wilder	Campbell	4	0.95
22	0200003	Fort Thomas	Campbell	0	0.00
23	0220056	Fort Thomas	Campbell	0	0.00
24	0220058	Fort Thomas	Campbell	0	0.00
25	0260001	Fort Thomas	Campbell	0	0.00
26	0270020	Fort Thomas	Campbell	0	0.00
27	0270026	Fort Thomas	Campbell	3	0.01
28	0270062	Fort Thomas	Campbell	0	0.00
29	0270103	Fort Thomas	Campbell	0	0.00
30	0280001	Fort Thomas	Campbell	1	0.00
31	0280073	Fort Thomas	Campbell	0	0.00
32	0360004	Dayton	Campbell	0	0.00
33	0360074	Dayton	Campbell	0	0.00
34	0380005	Fort Thomas	Campbell	3	0.02
35	0400002	Fort Thomas	Campbell	3	0.11
36	0400017	Fort Thomas	Campbell	0	0.00
37	0410010	Fort Thomas	Campbell	3	0.01
38	0410019	Fort Thomas	Campbell	3	0.01
39	0410036	Fort Thomas	Campbell	0	0.00
40	0430006	Newport	Campbell	3	0.01
41	0530083	Newport	Campbell	3	0.01
42	0860001	Wilder	Campbell	11	7.71
43	0860003	Wilder	Campbell	0	0.00
44	0860016	Wilder	Campbell	0	0.00
45	1010002	Fort Thomas	Campbell	0	0.00
46	1090069	Edgewood	Kenton	0	0.00
47	1110067	Erlanger	Kenton	0	0.00
48	1110161	Erlanger	Kenton	0	0.00
49	1110174	Elsmere	Kenton	0	0.00
50	1190012	Erlanger	Kenton	2	0.02

Recurring Wet Weather SSOs

No.	MHID	City	County	Model Predicted Overflow Activations	Model Predicted Overflow Volume (MG)
51	1220016	Erlanger	Kenton	2	0.00
52	1220054	Erlanger	Kenton	2	0.01
53	1240008	Erlanger	Kenton	0	0.00
54	1240012	Erlanger	Kenton	0	0.00
55	1550036	Fort Mitchell	Kenton	0	0.00
56	1550053	Fort Mitchell	Kenton	0	0.00
57	1560092	Fort Mitchell	Kenton	2	0.07
58	1560121	Fort Mitchell	Kenton	0	0.00
59	1700008	Covington	Kenton	0	0.00
60	1730086	Unicorp Kenton County	Kenton	1	0.00
61	1730100	Crescent Springs	Kenton	0	0.00
62	1730103	Fort Mitchell	Kenton	0	0.00
63	1760047	Edgewood	Kenton	1	0.00
64	1760048	Edgewood	Kenton	0	0.00
65	1790003	Crescent Springs	Kenton	0	0.00
66	1830067	Unicorp Boone County	Boone	0	0.00
67	1850140	Covington	Kenton	7	0.16
68	1850141	Covington	Kenton	10	0.57
69	1870013	Covington	Kenton	0	0.00
70	1870014	Covington	Kenton	0	0.00
71	1920086	Cold Spring	Campbell	0	0.00
72	1920097	Cold Spring	Campbell	2	0.00
73	1920163	Cold Spring	Campbell	0	0.00
74	1940006	Fort Wright	Kenton	0	0.00
75	1940038	Fort Wright	Kenton	2	0.00
76	1940039	Fort Wright	Kenton	2	0.02
77	1940044	Fort Wright	Kenton	2	0.02
78	1990018	Covington	Kenton	0	0.00
79	2020035	Taylor Mill	Kenton	0	0.00
80	2020203	Covington	Kenton	0	0.00
81	2070019	Elsmere	Kenton	0	0.00
82	2090008	Elsmere	Kenton	5	0.05
83	2100002	Elsmere	Kenton	0	0.00
84	2100007	Elsmere	Kenton	0	0.00
85	2100036	Elsmere	Kenton	0	0.00
86	2100037	Elsmere	Kenton	0	0.00
87	2100057	Elsmere	Kenton	0	0.00
88	2100128	Elsmere	Kenton	0	0.00
89	2100129	Elsmere	Kenton	4	0.04
90	2110002	Elsmere	Kenton	2	0.01
91	2110006	Elsmere	Kenton	0	0.00
92	2120001	Elsmere	Kenton	1	0.00
93	2120041	Elsmere	Kenton	0	0.00
94	2130026	Erlanger	Kenton	0	0.00
95	2130027	Erlanger	Kenton	0	0.00
96	2130028	Erlanger	Kenton	0	0.00
97	2170097	Crestview Hills	Kenton	0	0.00
98	2280023	Unicorp Kenton County	Kenton	0	0.00
99	2290001	Crescent Springs	Kenton	0	0.00

Recurring Wet Weather SSOs

No.	MHID	City	County	Model Predicted Overflow Activations	Model Predicted Overflow Volume (MG)
100	2300011	Erlanger	Kenton	0	0.00
101	2300016	Erlanger	Kenton	0	0.00
102	2300019	Erlanger	Kenton	0	0.00
103	2300121	Independence	Kenton	1	0.10
104	2300123	Unicorp Kenton County	Kenton	1	0.00
105	2301219	Erlanger	Kenton	1	0.00
106	2301274	Erlanger	Kenton	0	0.00
107	2370003	Unicorp Boone County	Boone	0	0.00
108	2400001	Unicorp Boone County	Boone	0	0.00
TOTAL				122	11.58

Threshold for model activation is 0.01 MGD and 0.001 MG

(This page intentionally left blank for double-sided printing.)

APPENDIX E:
Wet Weather CSOs

(This page intentionally left blank for double-sided printing.)

Wet Weather CSOs				
No.	CSO ID	KPDES Permit #	Model Predicted Activations	Model Predicted Overflow Volume (MG)
1	0010220	To Be Permitted	5	0.49
2	0030031	KY0021466 - Outfall 10	0	0.00
3	0200069	KY0021466 - Outfall 11	7	0.07
4	0330100	KY0021466 - Outfall 12	0	0.00
5	0340050	KY0021466 - Outfall 14	4	0.05
6	0340051	KY0021466 - Outfall 13	3	0.02
7	0360079	To Be Permitted	2	0.14
8	0540157	To Be Permitted	26	0.31
9	0540156	To Be Permitted	21	0.35
10	0540158	To Be Permitted	2	0.04
11	0550134	To Be Permitted	1	0.00
12	0570089	KY0021466 - Outfall 16	2	1.45
13	0570090	KY0021466 - Outfall 17	0	0.00
14	0600094	KY0021466 - Outfall 18	18	0.51
15	0600096	To Be Permitted	11	0.11
16	0600097	KY0021466 - Outfall 19	17	0.79
17	0600104	To Be Permitted	2	0.03
18	0610071	KY0021466 - Outfall 21	29	5.02
19	0610072	KY0021466 - Outfall 20	5	0.09
20	0620075	KY0021466 - Outfall 23	30	2.50
21	0620077	KY0021466 - Outfall 22	12	0.13
22	0630054	To Be Permitted	0	0.00
23	0630061	KY0021466 - Outfall 83	17	1.01
24	0640090	KY0021466 - Outfall 24	31	16.95
25	0650054	To Be Permitted	2	0.01
26	0650090	KY0021466 - Outfall 26	5	0.89
27	0650098	To Be Permitted	4	0.58
28	0650100	KY0021466 - Outfall 25	8	0.06
29	0660085	To Be Permitted	6	0.18
30	0690059	To Be Permitted	0	0.00
31	0690067	To Be Permitted	6	0.03
32	0730129	To Be Permitted	29	0.54
33	0770096	KY0021466 - Outfall 28	17	0.72
34	0790084	KY0021466 - Outfall 31	34	3.21
35	0790086	KY0021466 - Outfall 29	23	15.52
36	0840111	To Be Permitted	3	0.13
37	0840112	To Be Permitted	21	0.59
38	0840116	KY0021466 - Outfall 27	31	1.49
39	0870078	KY0021466 - Outfall 33	2	0.21
40	0870079	KY0021466 - Outfall 34	24	6.89
41	0880081	KY0021466 - Outfall 36	27	5.30
42	0880082	KY0021466 - Outfall 35	4	0.23
43	0890081	To Be Permitted	0	0.00
44	0910065	KY0021466 - Outfall 38	25	24.85

Wet Weather CSOs				
No.	CSO ID	KPDES Permit #	Model Predicted Activations	Model Predicted Overflow Volume (MG)
45	0910066	To Be Permitted	0	0.00
46	0910068	KY0021466 - Outfall 37	17	9.53
47	0910084	To Be Permitted	7	0.16
48	0930102	KY0021466 - Outfall 43	0	0.00
49	0930103	KY0021466 - Outfall 42	2	0.02
50	0930104	KY0021466 - Outfall 40	4	0.11
51	0930105	KY0021466 - Outfall 41	29	8.00
52	0930106	KY0021466 - Outfall 39	1	0.00
53	0960063	KY0021466 - Outfall 45	5	0.34
54	0960064	KY0021466 - Outfall 44	4	0.03
55	0980073	KY0021466 - Outfall 46	7	0.07
56	0980080	KY0021466 - Outfall 47	6	0.04
57	0980081	KY0021466 - Outfall 48	32	15.07
58	1320112	To Be Permitted	0	0.00
59	1350155	KY0021466 - Outfall 49	1	0.01
60	1380132	To Be Permitted	1	0.02
61	1380146	To Be Permitted	1	0.00
62	1420141	KY0021466 - Outfall 50	21	0.29
63	1420142	KY0021466 - Outfall 51	31	13.66
64	1420144	KY0021466 - Outfall 52	0	0.00
65	1420145	KY0021466 - Outfall 53	0	0.00
66	1420146	KY0021466 - Outfall 54	1	0.10
67	1420147	KY0021466 - Outfall 55	4	0.06
68	1440204	KY0021466 - Outfall 59	7	0.08
69	1440206	KY0021466 - Outfall 61	21	0.59
70	1440207	To Be Permitted	0	0.00
71	1440209	KY0021466 - Outfall 56	33	26.09
72	1440508	KY0021466 - Outfall 60	10	0.35
73	1470089	KY0021466 - Outfall 62	1	0.05
74	1470093	KY0021466 - Outfall 63	24	13.29
75	1480185	To Be Permitted	11	0.24
76	1480187	KY0021466 - Outfall 30	26	78.98
77	1490132	KY0021466 - Outfall 65	2	0.17
78	1490172	KY0021466 - Outfall 64	0	0.00
79	1500131	KY0021466 - Outfall 66	14	1.06
80	1510133	To Be Permitted	0	0.00
81	1710114	KY0021466 - Outfall 69	1	0.05
82	1710116	KY0021466 - Outfall 68	24	2.33
83	1710119	KY0021466 - Outfall 70	7	0.65
84	1710121	KY0021466 - Outfall 71	3	0.22
85	1710124	KY0021466 - Outfall 72	3	0.35
86	1720109	KY0021466 - Outfall 73	6	2.21
87	1730259	KY0021466 - Outfall 75	6	0.36
88	1730262	To Be Permitted	1	0.00

Wet Weather CSOs				
No.	CSO ID	KPDES Permit #	Model Predicted Activations	Model Predicted Overflow Volume (MG)
89	1730263	KY0021466 - Outfall 74	6	0.34
90	1840130	To Be Permitted	13	0.54
91	1850158	KY0021466 - Outfall 76	7	2.78
92	1870193	KY0021466 - Outfall 78	15	0.35
93	1870194	KY0021466 - Outfall 79	2	0.06
94	1880090	KY0021466 - Outfall 81	9	0.61
95	1880091	KY0021466 - Outfall 80	4	0.40
		TOTAL	946	271.15

Threshold for model activation is 0.01 MGD and 0.001 MG
